PINE CREEK OREGON, PLACER PROSPECTING

DATE July 1 1940

	Footage today	Footage To Date	Yardage Today	Yardage To Date	Number Samples	Average Recovery per Cu.Yd.	Recovery Today	Recovery To Date	Assessment Work Today	Assessment Work To Date	Preparatory Today	Preparatory To Date
Boulder shaft												
Preparatory											67.25	533.94
Sampling												
New Drifting												
Ingram Shaft												
Preparatory												74.63
Sampling												
New Drifting												
Assessment Work										74.40		
Prospect Shaft No. 1												
Preparatory												
Sinking												
East drift												
West drift												
Prospect Shaft No. 2												
Preparatory												
Sinking												
East drift												
West drift												
Justus Claim												
Assessment Work									4.50	72.77		

	To Day	To Date
Personnel	G	
Pay Roll	67.24	551.95
Mat. & Supplies (Approx.)		378.47
Other Expense (Approx.)	35.00	35.00
Total Expense (Approx.)	102.24	965.42

Trend of Pine Creek:

Weather: Warm with rain in evening.

Remarks: Boulder shaft has been pumped out. Found timbers in good state of preservation - some places requiring to be caught up. Are now ready to begin sampling. Mr Johnson and Mr Turner arrived from Boise to supervise sampling. We are having difficulty forcenting ourselves from the mafx of Pine Creek Placers as apparently considerable work was done since the map was made.

dead

CORNUCOPIA PLACERS
P.O. BOX 1617
BOISE, IDAHO 83702
(ITEM 3)

EXHIBIT "E"

PINE CREEK OREGON, PLACER PROSPECTING

DATE July 2 1940

	Footage today	Footage To Date	Yardage Today	Yardage To Date	Number Samples	Average Recovery per Cu.Yd.	Recovery Today	Recovery To Date	Assessment Work Today	Assessment Work To Date	Preparatory Today	Preparatory To Date
Boulder shaft												
Preparatory											77.08	611.02
Sampling												
New Drifting												
Ingram Shaft												
Preparatory												74.63
Sampling												
New Drifting												
Assessment Work										74.40		
Prospect Shaft No. 1												
Preparatory												
Sinking												
East drift												
West drift												
Prospect Shaft No. 2												
Preparatory												
Sinking												
East drift												
West drift												
Justus Claim												
Assessment Work										72.77		

	To Day	To Date
Personnel	11	
Pay Roll	77.24	629.19
Mat. & Supplies (Approx.)	24.69	403.16
Other Expense (Approx.)	25.00	60.00
Total Expense (Approx.)	126.93	1092.35

Trend of Pine Creek:

Weather: Clear & hot

Remarks: Sampling done only on day shift - using a rocker for the one cubic yard samples and are timbering in sets for the larger samples. Power failure at 5.50 P.M. Unable to start pump during night.

PINE CREEK OREGON, PLACER PROSPECTING

DATE July 3 1940

	Footage today	Footage To Date	Yardage Today	Yardage To Date	Number Samples	Average Recovery per Cu.Yd.	Recovery Today	Recovery To Date	Assessment Work Today	Assessment Work To Date	Preparatory Today	Preparatory To Date
Boulder shaft												
Preparatory											62.48	673.50
Sampling												
New Drifting												
Ingram Shaft												
Preparatory												74.63
Sampling												
New Drifting												
Assessment Work										74.40		
Prospect Shaft No. 1												
Preparatory												
Sinking												
East drift												
West drift												
Prospect Shaft No. 2												
Preparatory												
Sinking												
East drift												
West drift												
Justus Claim												
Assessment Work									4.50	77.27		

	To Day	To Date
Personnel	13	
Pay Roll	87.78	716.97
Mat. & Supplies (Approx.)	43.50	446.66
Other Expense (Approx.)	25.00	85.00
Total Expense (Approx.)	156.28	1248.63

Trend of Pine Creek:

Weather: Clear and hot.

Remarks: Worked all day repairing pump and hoisting same in and out of shaft. Two other sinking pumps on this locality and both are out of order. Too much water in mine to take samples. Built another sacker to-day to speed up work.
Mr Johnson and Mr Turner returned to Boise.

PINE CREEK OREGON, PLACER PROSPECTING

DATE July 4 1940

	Footage today	Footage To Date	Yardage Today	Yardage To Date	Number Samples	Average Recovery per Cu.Yd.	Recovery Today	Recovery To Date	Assessment Work Today	Assessment Work To Date	Preparatory Today	Preparatory To Date
Boulder shaft												
Preparatory											33.26	706.76
Sampling												
New Drifting												
Ingram Shaft												
Preparatory												74.63
Sampling												
New Drifting												
Assessment Work										74.40		
Prospect Shaft No. 1												
Preparatory												
Sinking												
East drift												
West drift												
Prospect Shaft No. 2												
Preparatory												
Sinking												
East drift												
West drift												
Justus Claim												
Assessment Work										77.27		

	To Day	To Date
Personnel	6	
Pay Roll	51.15	768.12
Mat. & Supplies (Approx.)		446.66
Other Expense (Approx.)	10.00	95.00
Total Expense (Approx.)	61.15	1309.78

Trend of Pine Creek:

Weather: Clear and hot

Remarks: No work to-day except pump-men

PINE CREEK OREGON, PLACER PROSPECTING

DATE July 5 1940

	Footage today	Footage To Date	Yardage Today	Yardage To Date	Number Samples	Average Recovery per Cu.Yd.	Recovery Today	Recovery To Date	Assessment Work Today	Assessment Work To Date	Preparatory Today	Preparatory To Date
Boulder shaft											47.21	753.97
Preparatory												
Sampling												
New Drifting												
Ingram Shaft												74.63
Preparatory												
Sampling												
New Drifting												
Assessment Work									9.00	83.40		
Prospect Shaft No. 1												
Preparatory												
Sinking												
East drift												
West drift												
Prospect Shaft No. 2												
Preparatory												
Sinking												
East drift												
West drift												
Justus Claim												
Assessment Work									4.50	81.77		

	To Day	To Date
Personnel	11	
Pay Roll	77.23	845.35
Mat. & Supplies (Approx.)		466.66
Other Expense (Approx.)	35.00	130.00
Total Expense (Approx.)	112.23	1442.01

Trend of Pine Creek:

Weather: Warm and clear

Remarks: Last parts of three pumps into one which is now working satisfactorily. Mr Johnson & Mr Turner expected back to night & sampling can be resumed to morrow. Crew cleaning out and timbering up where new samples are to be taken.

PINE CREEK OREGON, [illegible]ER PROSPECTING

DATE July 6 1940

	Footage today	Footage To Date	Yardage Today	Yardage To Date	Number Samples	Average Recovery per Cu.Yd.	Recovery Today	Recovery To Date	Assess-ment Work Today	Assess-ment Work To Date	Preparatory Today	Preparatory To Date
Boulder shaft												
Preparatory												[illegible]
Sampling			6	6	3	$1.20	$7.[illegible]	$7.21				
New Drifting												
Ingram Shaft												
Preparatory												[illegible]
Sampling												
New Drifting												
Assessment Work										53.40		
Prospect Shaft No. 1												
Preparatory												
Sinking												
East drift												
West drift												
Prospect Shaft No. 2												
Preparatory												
Sinking												
East drift												
West drift												
Justus Claim												
Assessment Work										81.77		

	To Day	To Date	Trend of Pine Creek:	Weather: Warm and clear
Personnel	13		Remarks: Sampling resumed with three men. Also completed two one	
Pay Roll	10.98	105.33	one cubic yard boxes with sluices and the other one four	
Mat. & Supplies (Approx.)		446.26	cubic yard boxes shoring ties to surface and sluicing	
Other Expense (Approx.)	5.00	165.03	stone found no cemented gravels. Stones are average material that	
			I believe same can be satisfactorily handled with a fork or fine	
Total Expense (Approx.)	144.[illegible]	1[illegible]6.99	cubic yard electric shovel	

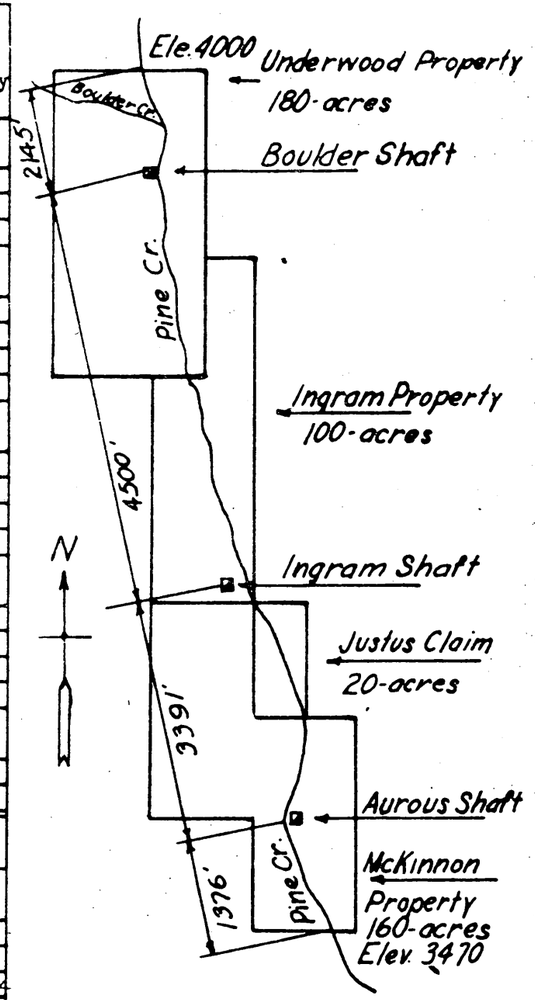

PINE CREEK OREGON, PLACER PROSPECTING

DATE Jan. 7 1940

	Footage today	Footage To Date	Yardage Today	Yardage To Date	Number Samples	Average Recovery per Cu.Yd.	Recovery Today	Recovery To Date	Assess-ment Work Today	Assess-ment Work To Date	Preparatory Today	Preparatory To Date
Boulder shaft												
Preparatory												
Sampling			4	10	4	$0.96	$3.84	$11.35				753.97
New Drifting												
Ingram Shaft												
Preparatory												
Sampling												74.63
New Drifting												
Assessment Work									4.50	87.90		
Prospect Shaft No. 1												
Preparatory												
Sinking												
East drift												
West drift												
Prospect Shaft No. 2												
Preparatory												
Sinking												
East drift												
West drift												
Justus Claim												
Assessment Work									4.50	86.27		

	To Day	To Date
Personnel	15	
Pay Roll	98.32	1053.65
Mat. & Supplies (Approx.)		466.66
Other Expense (Approx.)	35.00	200.00
Total Expense (Approx.)	133.32	1720.31

Trend of Pine Creek:

Weather: Warm and clear

Remarks: These four samples taken on the Northerly part of old workings. Line tentatively established by Mr Patterson showed up to be fifty yards.

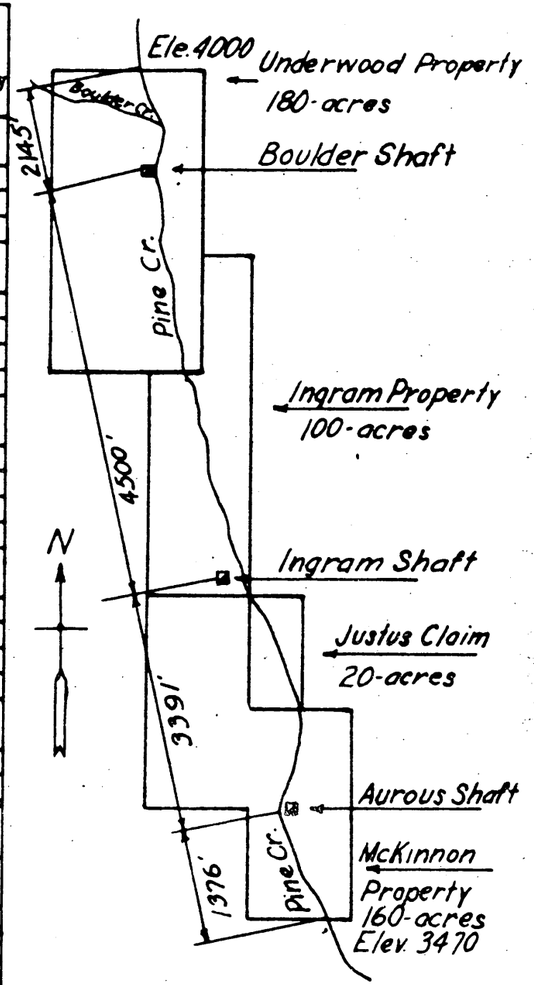

PINE CREEK OREGON, PLACER PROSPECTING

DATE July 8 1940

	Footage today	Footage To Date	Yardage Today	Yardage To Date	Number Samples	Average Recovery per Cu.Yd.	Recovery Today	Recovery To Date	Assessment Work Today	Assessment Work To Date	Preparatory Today	Preparatory To Date
Boulder shaft												
Preparatory												753.97
Sampling			10.6	20.6	4	$1.56	$16.63	$27.98				
New Drifting												
Ingram Shaft												
Preparatory												74.63
Sampling												
New Drifting												
Assessment Work									4.50	92.40		
Prospect Shaft No. 1												
Preparatory												
Sinking												
East drift												
West drift												
Prospect Shaft No. 2												
Preparatory												
Sinking												
East drift												
West drift												
Justus Claim												
Assessment Work									4.50	90.27		

	To Day	To Date
Personnel	14	
Pay Roll	94.44	1148.09
Mat. & Supplies (Approx.)		466.66
Other Expense (Approx.)	30.00	230.00
Total Expense (Approx.)	124.44	1844.75

Trend of Pine Creek:

Weather: Warm and clear

Remarks: One 1 cu yard sample to day taken in Northerly part of old workings produced $11.53 with one nugget worth $4.49. This is the largest single piece of gold yet secured. Timbering started in old workings South of the shaft where 4 cubic yards per sample will be taken out and sluiced.

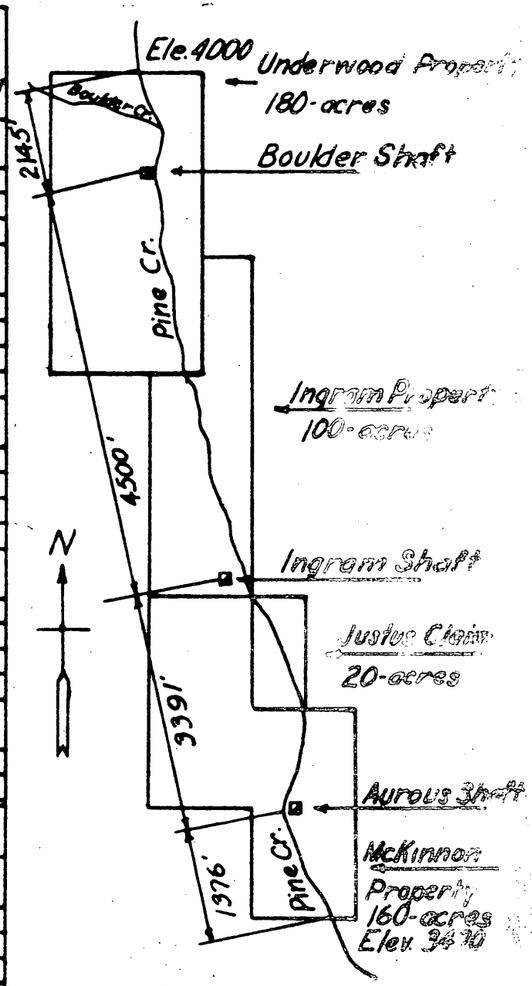

PINE CREEK OREGON, PLACER PROSPECTING

DATE July 9 1940

	Footage today	Footage To Date	Yardage Today	Yardage To Date	Number Samples	Average Recovery per Cu.Yd.	Recovery Today	Recovery To Date	Assess-ment Work Today	Assess-ment Work To Date	Preparatory Today	Preparatory To Date
Boulder shaft												
Preparatory												
Sampling			4	24.6	3	$0.385	$1.54	$29.52				753.97
New Drifting												
Ingram Shaft												
Preparatory												
Sampling												
New Drifting												74.63
Assessment Work												
Prospect Shaft No. 1									4.50	96.90		
Preparatory												
Sinking												
East drift												
West drift												
Prospect Shaft No. 2												
Preparatory												
Sinking												
East drift												
West drift												
Justus Claim												
Assessment Work												
									4.50	94.77		

	To Day	To Date
Personnel	14	
Pay Roll	93.33	1241.42
Mat. & Supplies (Approx.)	38.34	505.00
Other Expense (Approx.)	21.00	251.00
Total Expense (Approx.)	152.67	1997.42

Trend of Pine Creek:

Weather: Warm and clear

Remarks: We are driving a full size cross cut South of the shaft heading slightly down stream. This will not be terminated until about around July 11th. We expect to finish sampling this shaft on July 12th. One sample of 2 cu yds taken in the North Main drift showed only two colors

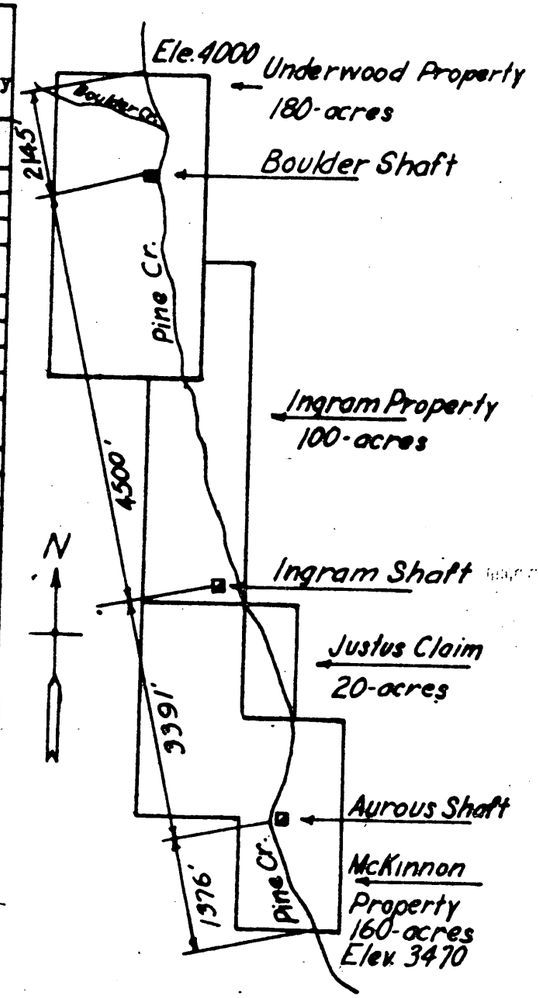

PINE CREEK OREGON, PLACER PROSPECTING

DATE July 10 1940

	Footage today	Footage To Date	Yardage Today	Yardage To Date	Number Samples	Average Recovery per Cu.Yd.	Recovery Today	Recovery To Date	Assessment Work Today	Assessment Work To Date	Preparatory Today	Preparatory To Date
Boulder shaft												753.97
Preparatory												
Sampling			12.6	37.2	4	3.81	48.05	77.57				
New Drifting												
Ingram Shaft												108.74
Preparatory												
Sampling												
New Drifting												
Assessment Work									4.50	101.40		
Prospect Shaft No. 1												
Preparatory												
Sinking												
East drift												
West drift												
Prospect Shaft No. 2												
Preparatory												
Sinking												
East drift												
West drift												
Justus Claim												
Assessment Work									4.50	99.27		

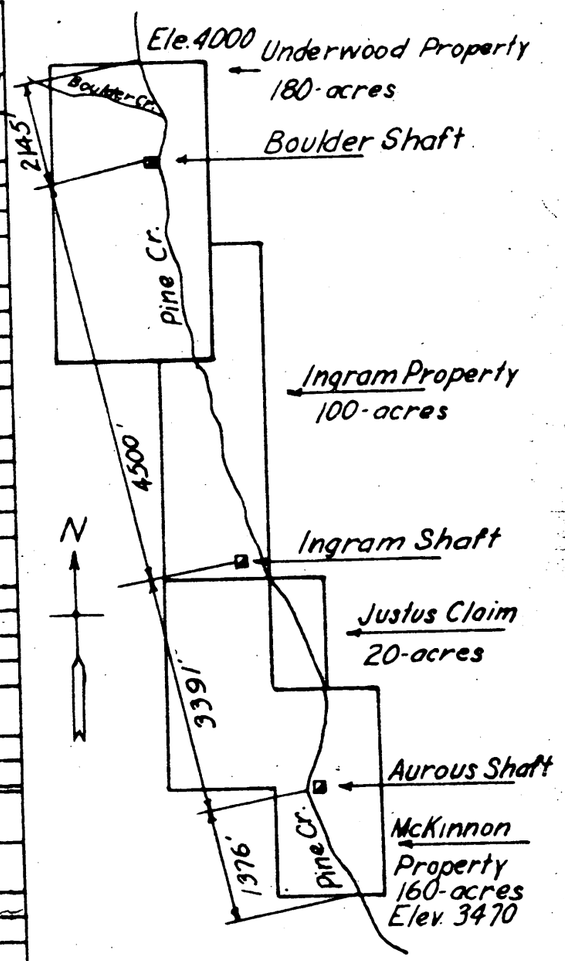

	To Day	To Date
Personnel	16	
Pay Roll	176.58	1418.00
Mat. & Supplies (Approx.)	24.11	529.11
Other Expense (Approx.)	10.00	261.00
Total Expense (Approx.)	210.69	2208.11

Trend of Pine Creek:

Weather: Warm and clear

Remarks: To-days samples are the best consistent samples yet taken. We have not been able to ever come close to the values shown as recovered by Mr. Pattison in 1936. We are not familiar with his method of sampling but believe our samples to be substantially correct as we are endeavoring to use utmost precaution both in measurements and recovery.

PINE CREEK OREGON, PLACER PROSPECTING

DATE July 11 1940

	Footage today	Footage To Date	Yardage Today	Yardage To Date	Number Samples	Average Recovery per Cu.Yd.	Recovery Today	Recovery To Date	Assess-ment Work Today	Assess-ment Work To Date	Preparatory Today	Preparatory To Date
Boulder shaft												
Preparatory												753.97
Sampling			0.15	37.35	1	18.80	2.82	80.39				
New Drifting												
Ingram Shaft												
Preparatory											10.00	118.74
Sampling												
New Drifting												
Assessment Work									4.50	105.40		
Prospect Shaft No. 1												
Preparatory												
Sinking												
East drift												
West drift												
Prospect Shaft No. 2												
Preparatory												
Sinking												
East drift												
West drift												
Justus Claim												
Assessment Work									4.50	103.77		

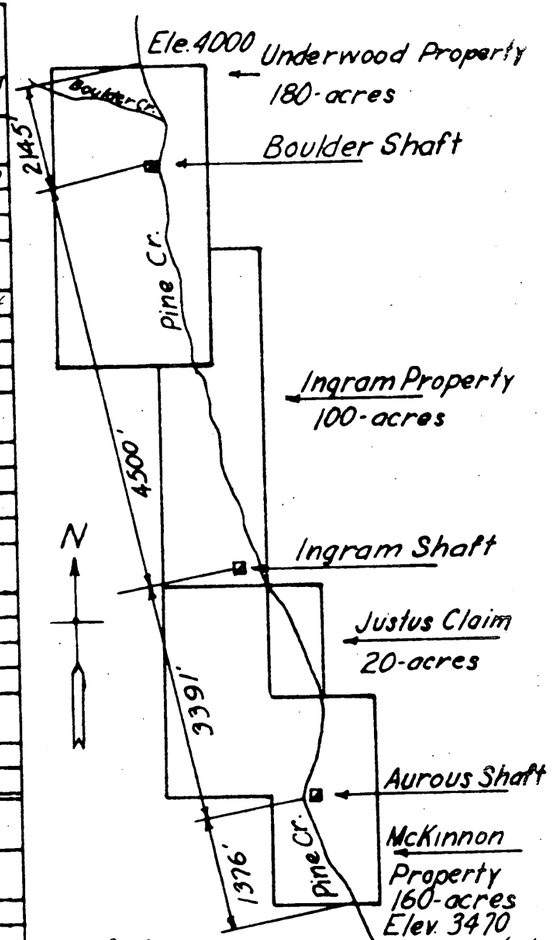

	To Day	To Date
Personnel	15	
Pay Roll	101.10	1519.10
Mat. & Supplies (Approx.)		524.11
Other Expense (Approx.)	10.00	271.00
Total Expense (Approx.)	111.10	2319.21

Trend of Pine Creek:

Weather: Warm and clear

Remarks: Sampling has now been completed on Boulder Shaft workings. We are moving to Ingram Shaft. A total of 19 samples were taken on the area from bed rock to six feet higher. These average 2.15 per cu yd measured in place. In addition to these samples one roof sample was taken just above the top of the drift which ran ten cents per cu yd. These shaft samples were taken at the following elevations above Bed Rock.

Elev 10' Shaft Sample #1 General Sample #14 = $0.40 per cu yd
" 25' " " #2 " " #15 = .02 " " "
" 37' " " #3 " " #16 = .015 " " "

Bed Rock cu yd samples averaged 6.63
Next yd above bed rock averaged .44
Next 5 yds up the shaft figured to average .25
Next 5 " " " " " " .15
Next 6 " " " " " " .015
On this basis the ground would average from surface to Bed Rock $0.44 per cu yd

PINE CREEK OREGON, PLACER PROSPECTING

DATE July 12 1940

	Footage today	Footage To Date	Yardage Today	Yardage To Date	Number Samples	Average Recovery per Cu.Yd.	Recovery Today	Recovery To Date	Assessment Work Today	Assessment Work To Date	Preparatory Today	Preparatory To Date
Boulder shaft												
Preparatory												753.97
Sampling												
New Drifting												
Ingram Shaft												
Preparatory											138.26	257.00
Sampling												
New Drifting												
Assessment Work									64.04	169.94		
Prospect Shaft No. 1												
Preparatory												
Sinking												
East drift												
West drift												
Prospect Shaft No. 2												
Preparatory												
Sinking												
East drift												
West drift												
Justus Claim												
Assessment Work										103.77		

	To Day	To Date
Personnel	12	
Pay Roll	85.00	1604.10
Mat. & Supplies (Approx.)	43.26	572.37
Other Expense (Approx.)	10.00	281.00
Total Expense (Approx.)	138.26	2457.47

Trend of Pine Creek:

Weather: Warm and clear

Remarks: Moving pumps, transformers, hoist and sundry equipment from Boulder Shaft to Ingram Shaft. Started pumping at 2.30 P.M. and best guess is that it will take 48 hours to pump out. Assessment work on Justus claim has been completed.

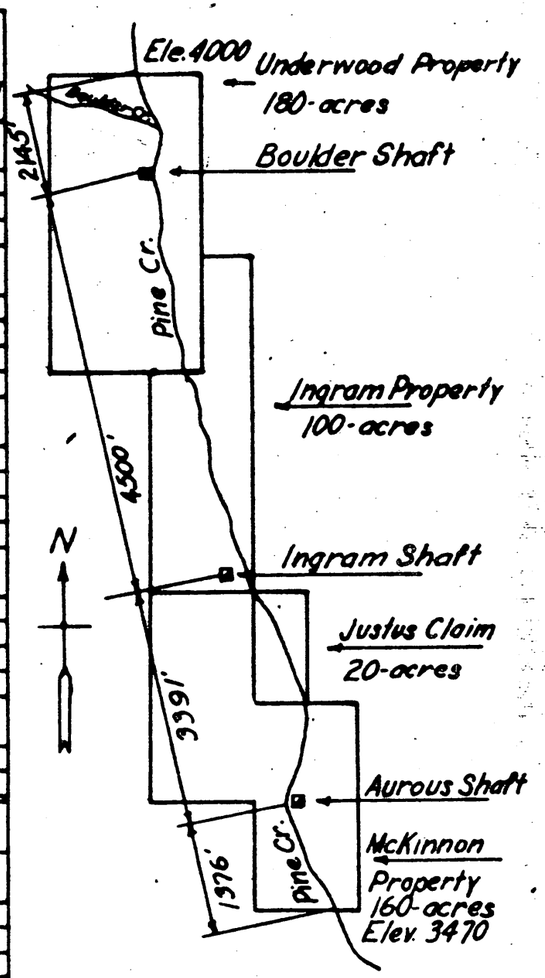

PINE CREEK OREGON, PLACER PROSPECTING

DATE July 13 1940

	Footage today	Footage To Date	Yardage Today	Yardage To Date	Number Samples	Average Recovery per Cu.Yd.	Recovery Today	Recovery To Date	Assessment Work Today	Assessment Work To Date	Preparatory Today	Preparatory To Date
Boulder shaft												
Preparatory												753.47
Sampling												
New Drifting												
Ingram Shaft												
Preparatory											103.31	360.31
Sampling												
New Drifting												
Assessment Work									67.84	237.78		
Prospect Shaft No. 1												
Preparatory												
Sinking												
East drift												
West drift												
Prospect Shaft No. 2												
Preparatory												
Sinking												
East drift												
West drift												
Justus Claim												
Assessment Work										103.77		

	To Day	To Date
Personnel	13	
Pay Roll	91.11	1695.21
Mat. & Supplies (Approx.)		572.37
Other Expense (Approx.)	12.20	293.20
Total Expense (Approx.)	103.31	2560.78

Trend of Pine Creek:

Weather: Warm and clear

Remarks: Moving and setting up equipment at Ingram shaft. Water going down in good shape. Plan to shut in second pump to-morrow morning and to be able to begin sampling by Monday morning or Monday noon.

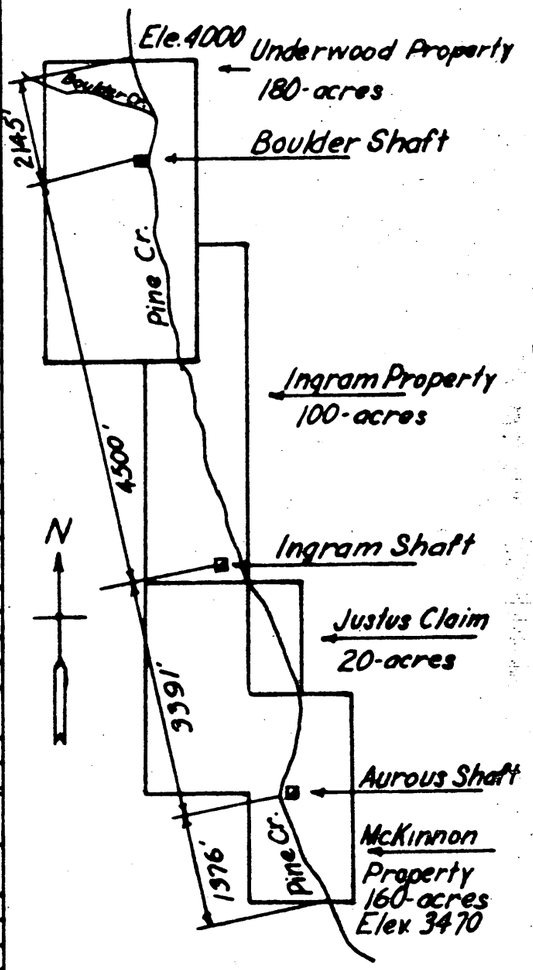

PINE CREEK OREGON, PLACER PROSPECTING

DATE July 14 1940

	Footage today	Footage To Date	Yardage Today	Yardage To Date	Number Samples	Average Recovery per Cu.Yd.	Recovery Today	Recovery To Date	Assessment Work Today	Assessment Work To Date	Preparatory Today	Preparatory To Date
Boulder shaft												
Preparatory												753.97
Sampling												
New Drifting												
Ingram Shaft												
Preparatory											101.11	461.42
Sampling												
New Drifting												
Assessment Work									67.84	305.62		
Prospect Shaft No. 1												
Preparatory												
Sinking												
East drift												
West drift												
Prospect Shaft No. 2												
Preparatory												
Sinking												
East drift												
West drift												
Justus Claim												
Assessment Work										103.77		

	To Day	To Date
Personnel	13	
Pay Roll	91.11	1786.32
Mat. & Supplies (Approx.)		572.37
Other Expense (Approx.)	10.00	303.20
Total Expense (Approx.)	101.11	2661.89

Trend of Pine Creek:

Weather: Warm and clear.

Remarks: Second pump just called. Water not going down as fast as we are approaching tunnel level. Apparently shaft is making more water than we anticipated from auth. ranger reports as we could get locally.

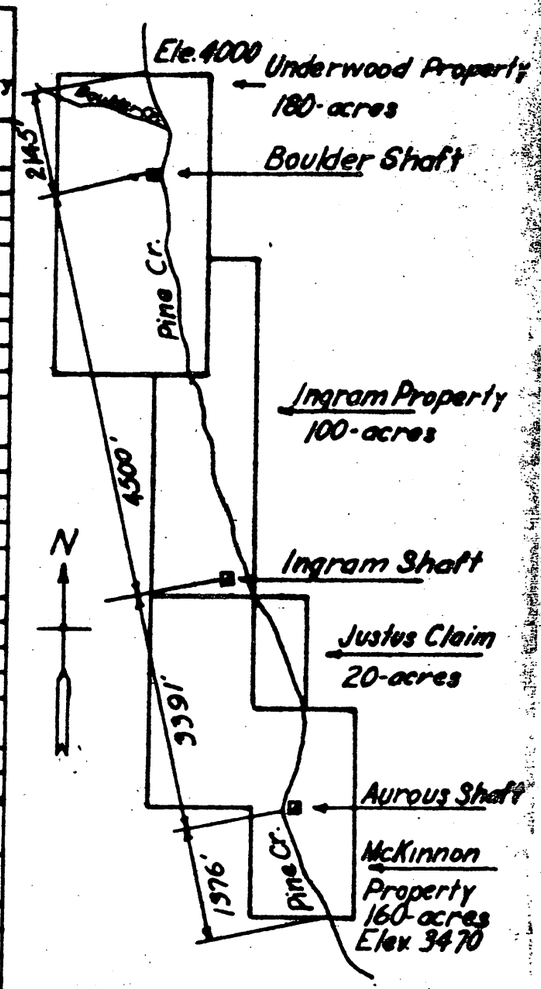

PINE CREEK OREGON, PLACER PROSPECTING

DATE July 15 1940

	Footage today	Footage To Date	Yardage Today	Yardage To Date	Number Samples	Average Recovery per Cu.Yd.	Recovery Today	Recovery To Date	Assessment Work Today	Assessment Work To Date	Preparatory Today	Preparatory To Date
Boulder shaft												
Preparatory												753.97
Sampling												
New Drifting												
Ingram Shaft												
Preparatory											93.34	554.76
Sampling												
New Drifting												
Assessment Work									50.07	355.69		
Prospect Shaft No. 1												
Preparatory												
Sinking												
East drift												
West drift												
Prospect Shaft No. 2												
Preparatory												
Sinking												
East drift												
West drift												
Justus Claim												
Assessment Work										103.77		

	To Day	To Date
Personnel	13	
Pay Roll	83.34	1869.66
Mat. & Supplies (Approx.)		572.37
Other Expense (Approx.)	10.00	313.20
Total Expense (Approx.)	93.34	2755.23

Trend of Pine Creek:

Weather: Warm and clear

Remarks: The two pumps which we have on hand are not sufficient to drain workings and we were not able to get very far underground to day. We are ordering two new pumps from Portland to morrow morning and we are installing discharge pipe in the shaft for that pumps. Crew will be reduced in accordance with conditions

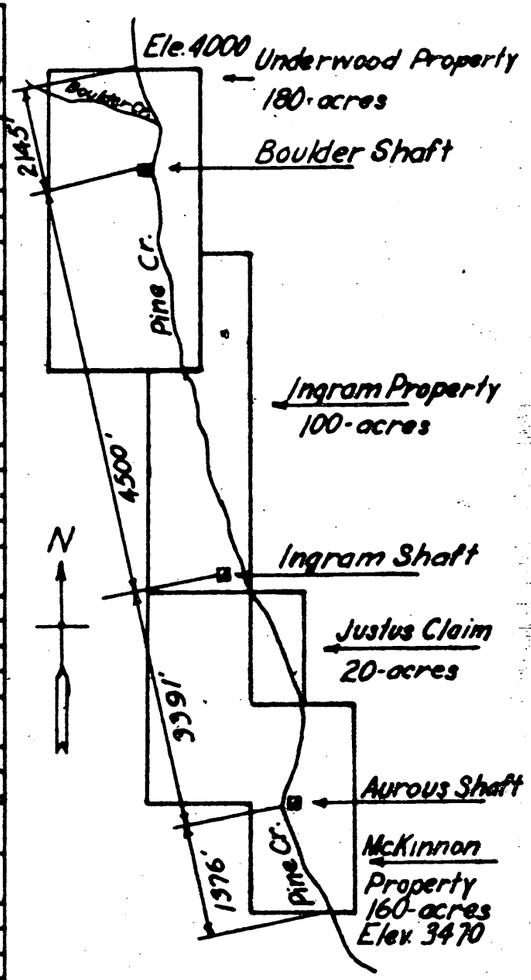

PINE CREEK OREGON, PLACER PROSPECTING

DATE July 16 1940

	Footage today	Footage To Date	Yardage Today	Yardage To Date	Number Samples	Average Recovery per Cu.Yd.	Recovery Today	Recovery To Date	Assessment Work Today	Assessment Work To Date	Preparatory Today	Preparatory To Date
Boulder shaft												
Preparatory												753.97
Sampling												
New Drifting												
Ingram Shaft												
Preparatory											97.20	651.96
Sampling												
New Drifting												
Assessment Work									57.30	412.99		
Prospect Shaft No. 1												
Preparatory												
Sinking												
East drift												
West drift												
Prospect Shaft No. 2												
Preparatory												
Sinking												
East drift												
West drift												
Justus Claim												
Assessment Work										103.77		

	To Day	To Date
Personnel	11	
Pay Roll	80.56	1950.22
Mat. & Supplies (Approx.)	6.64	579.01
Other Expense (Approx.)	10.00	323.20
Total Expense (Approx.)	97.20	2852.43

Trend of Pine Creek:

Weather: Cloudy with rain at night

Remarks:

Ordered pumps to-day which will arrive before noon Wednesday. Pipe, wiring and switches are all set for their installation when they arrive. Will organize to work two rockers two shifts each, as well as take drift samples.

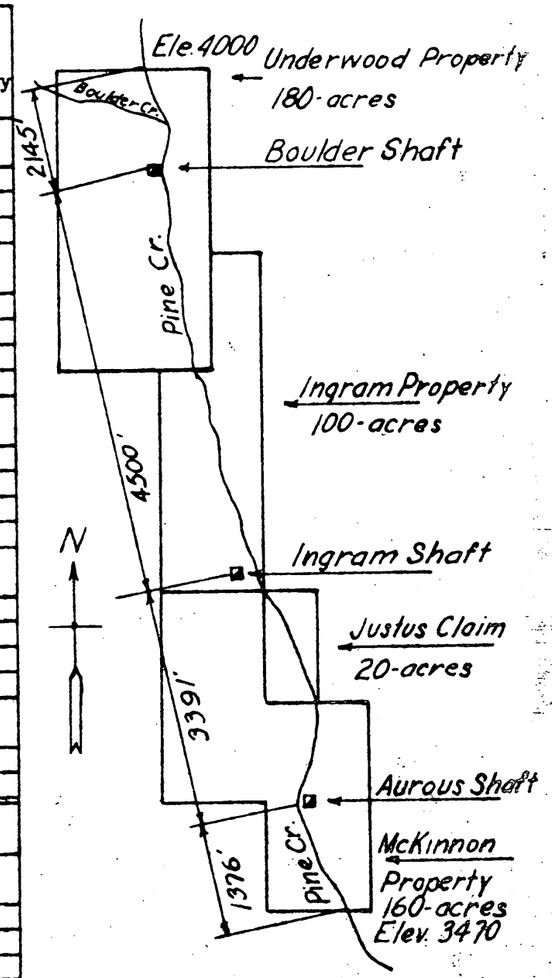

PINE CREEK OREGON, PLACER PROSPECTING

DATE July 17 1940

	Footage today	Footage To Date	Yardage Today	Yardage To Date	Number Samples	Average Recovery per Cu.Yd.	Recovery Today	Recovery To Date	Assessment Work Today	Assessment Work To Date	Preparatory Today	Preparatory To Date
Boulder shaft												
Preparatory												
Sampling												753.99
New Drifting												
Ingram Shaft												
Preparatory												
Sampling											219.19	371.15
New Drifting												
Assessment Work												
									28.83	495.82		
Prospect Shaft No. 1												
Preparatory												
Sinking												
East drift												
West drift												
Prospect Shaft No. 2												
Preparatory												
Sinking												
East drift												
West drift												
Justus Claim												
Assessment Work												
										193.77		

	To Day	To Date
Personnel	16	
Pay Roll	108.09	2086.31
Mat. & Supplies (Approx.)	93.10	672.11
Other Expense (Approx.)	20.00	313.20
Total Expense (Approx.)	219.19	3071.62

Trend of Pine Creek:

Remarks: Installing new pumps.

Weather: Cloudy and cooler

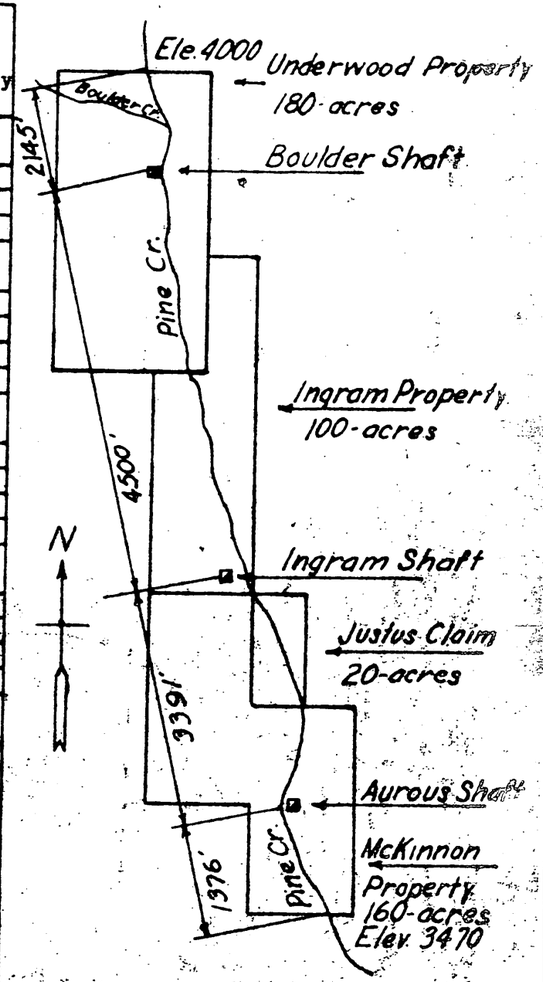

PINE CREEK OREGON, PLACER PROSPECTING

DATE July 29 1940

	Footage today	Footage To Date	Yardage Today	Yardage To Date	Number Samples	Average Recovery per Cu.Yd.	Recovery Today	Recovery To Date	Assessment Work Today	Assessment Work To Date	Preparatory Today	Preparatory To Date
Boulder shaft												
Preparatory												753.92
Sampling												
New Drifting												
Ingram Shaft												
Preparatory											101.76	972.91
Sampling												
New Drifting												
Assessment Work									15.00	510.82		
Prospect Shaft No. 1												
Preparatory												
Sinking												
East drift												
West drift												
Prospect Shaft No. 2												
Preparatory												
Sinking												
East drift												
West drift												
Justus Claim												
Assessment Work										103.77		

	To Day	To Date
Personnel	17	
Pay Roll	113.50	2169.30
Mat. & Supplies (Approx.)		672.11
Other Expense (Approx.)	20.00	363.20
Total Expense (Approx.)	133.50	3205.81

Trend of Pine Creek:

Weather: Cloudy & Cool

Remarks: Heavy electrical storm last night shut off power for 3½ hours and flooded drift. Completed pump installation and started timbering on night shift preparatory to starting sampling tomorrow.

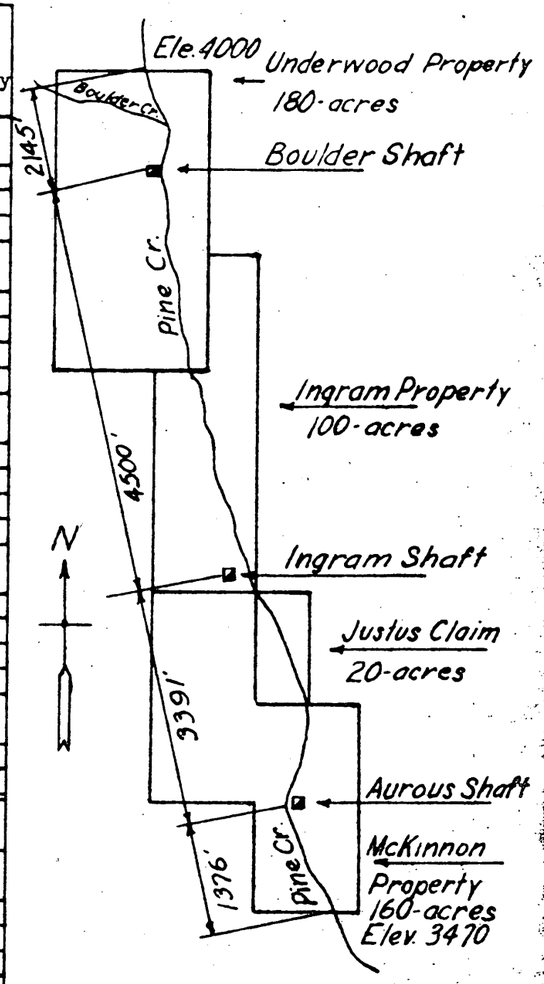

PINE CREEK OREGON, PLACER PROSPECTING

DATE July 19 1940

	Footage today	Footage To Date	Yardage Today	Yardage To Date	Number Samples	Average Recovery per Cu.Yd.	Recovery Today	Recovery To Date	Assessment Work Today	Assessment Work To Date	Preparatory Today	Preparatory To Date
Boulder shaft												
Preparatory												753.97
Sampling												
New Drifting												
Ingram Shaft												
Preparatory												972.91
Sampling												
New Drifting												
Assessment Work										510.82		
Prospect Shaft No. 1												
Preparatory												
Sinking												
East drift												
West drift												
Prospect Shaft No. 2												
Preparatory												
Sinking												
East drift												
West drift												
Justus Claim												
Assessment Work										103.77		

	To Day	To Date
Personnel	18	
Pay Roll	117.19	2287.09
Mat. & Supplies (Approx.)	1.32	673.43
Other Expense (Approx.)	20.00	383.20
Total Expense (Approx.)	138.51	3343.72

Trend of Pine Creek:

Weather:

Remarks: Continued timbering and preparing underground workings such as clearing drifts of boulders and other debris in order to move new material to the shaft. Mine had been left in very bad condition.

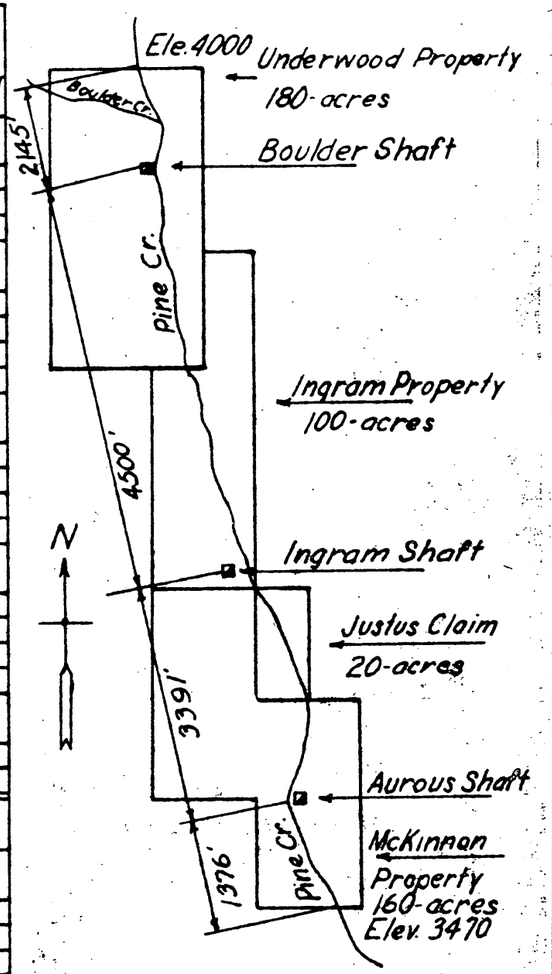

PINE CREEK OREGON, PLACER PROSPECTING

DATE ~~July 3,~~ 1940

	Footage today	Footage To Date	Yardage Today	Yardage To Date	Number Samples	Average Recovery per Cu.Yd.	Recovery Today	Recovery To Date	Assessment Work Today	Assessment Work To Date	Preparatory Today	Preparatory To Date
Boulder shaft												
Preparatory												
Sampling												~~955.97~~
New Drifting												
Ingram Shaft												
Preparatory												
Sampling												~~977.91~~
New Drifting												
Assessment Work										~~310.00~~		
Prospect Shaft No. 1												
Preparatory												
Sinking												
East drift												
West drift												
Prospect Shaft No. 2												
Preparatory												
Sinking												
East drift												
West drift												
Justus Claim												
Assessment Work										~~103.79~~		

	To Day	To Date
Personnel	~~19~~	
Pay Roll	~~111.64~~	~~3793.73~~
Mat. & Supplies (Approx.)		~~573.64~~
Other Expense (Approx.)	~~20.00~~	~~425.19~~
Total Expense (Approx.)	~~131.64~~	~~3695.56~~

Trend of Fine Creek:

Weather: ~~Cloudy and cooler~~

Remarks: ~~Sluicing has been started and material being moved to the surface for sluicing. First clean-up on complex will be made tomorrow. Dam dogs are holding water level down to our satisfaction.~~

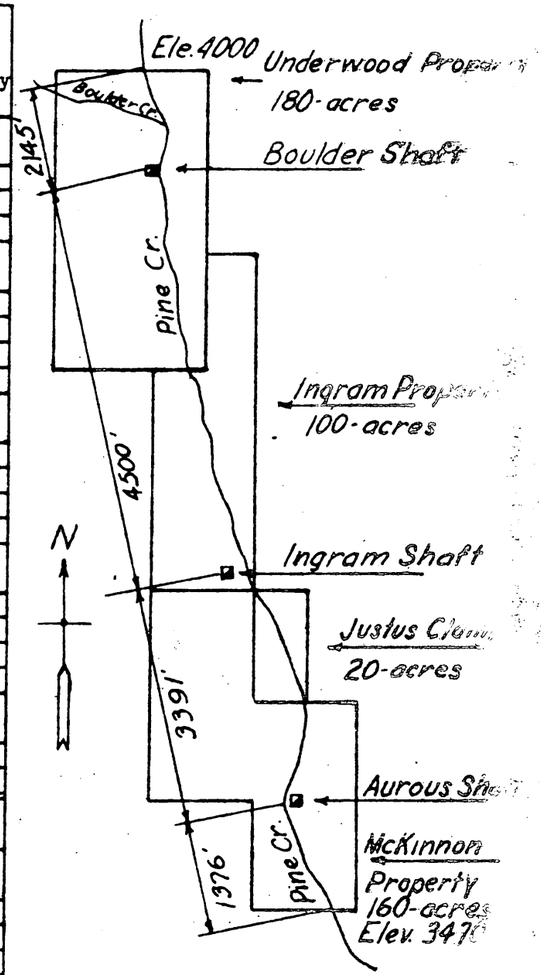

PINE CREEK OREGON, PLACER PROSPECTING

DATE July 21 1940

	Footage today	Footage To Date	Yardage Today	Yardage To Date	Number Samples	Average Recovery per Cu.Yd.	Recovery Today	Recovery To Date	Assessment Work Today	Assessment Work To Date	Preparatory Today	Preparatory To Date
Boulder shaft												
Preparatory												753.37
Sampling				37.35	12	2.15		80.39				
New Drifting												
Ingram Shaft												
Preparatory												972.31
Sampling			13.29	13.29	5	1.76	23.44	23.44				
New Drifting												
Assessment Work										510.82		
Prospect Shaft No. 1												
Preparatory												
Sinking												
East drift												
West drift												
Prospect Shaft No. 2												
Preparatory												
Sinking												
East drift												
West drift												
Justus Claim												
Assessment Work										103.77		

	To Day	To Date
Personnel	17	
Pay Roll	113.23	2512.98
Mat. & Supplies (Approx.)		673.63
Other Expense (Approx.)	20.00	423.50
Total Expense (Approx.)	133.23	3608.61

Trend of Pine Creek:

Weather: clear and hot

Remarks: Three of the above samples were taken in ground which was entirely different in character than the regular Pine Creek wash and very little results were expected, which proved correct. One sample of 2.16 cu yds ran $6.15 per cu yd. Another sample taken at about 3 feet above bedrock ran $ 1.16 per cu yd indicating that the material up to 7 feet above bedrock contained good values. As the gold in these workings is somewhat smaller, and the canyon wider, it is believed that the values may be distributed higher in the material.

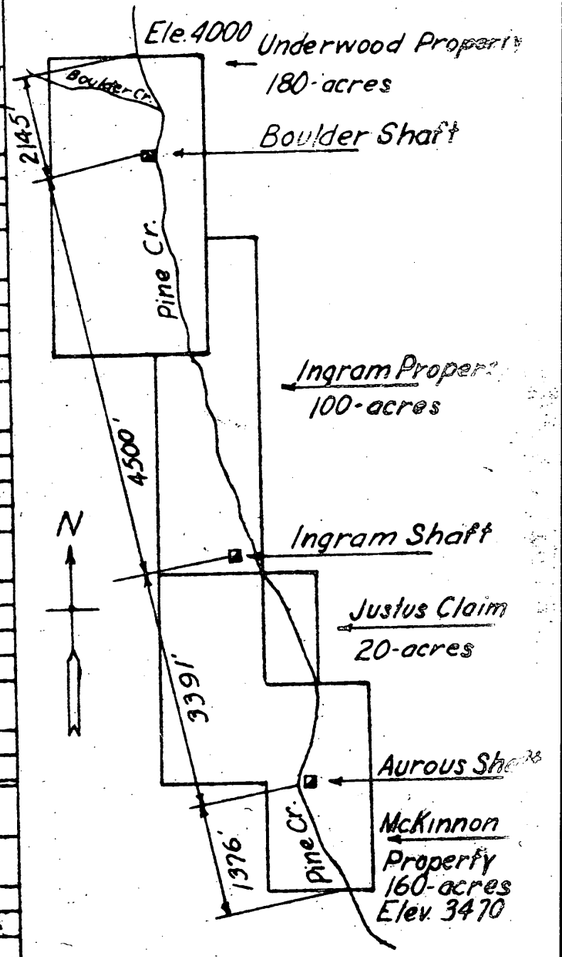

PINE CREEK OREGON, PLACER PROSPECTING

DATE July 28 1940

	Footage today	Footage To Date	Yardage Today	Yardage To Date	Number Samples	Average Recovery per Cu.Yd. TO DATE.	Recovery Today	Recovery To Date	Assessment Work Today	Assessment Work To Date	Preparatory Today	Preparatory To Date
Boulder shaft												
Preparatory												~~[illegible]~~
Sampling				~~[illegible]~~	~~19~~	~~2.15~~		~~[illegible]~~				
New Drifting												
Ingram Shaft												
Preparatory												
Sampling												~~973.91~~
New Drifting			~~5.01~~	~~18.70~~	~~2~~	~~8.20~~	~~16.59~~	~~40.52~~				
Assessment Work										~~510.02~~		
Prospect Shaft No. 1												
Preparatory												
Sinking												
East drift												
West drift												
Prospect Shaft No. 2												
Preparatory												
Sinking												
East drift												
West drift												
Justus Claim												
Assessment Work										103.77		

	To Day	To Date
Personnel	18	
Pay Roll	~~118.88~~	~~2630.84~~
Mat. & Supplies (Approx.)		~~373.43~~
Other Expense (Approx.)	~~20.00~~	~~443.20~~
Total Expense (Approx.)	~~138.88~~	~~3747.47~~

Trend of Pine Creek:

Weather: ~~Clear & hot~~

Remarks: ~~It is necessary to remove and replace considerable timbering in the various drifts in order that new places may be opened up under safe working conditions. Sampling is being carried on simultaneously.~~

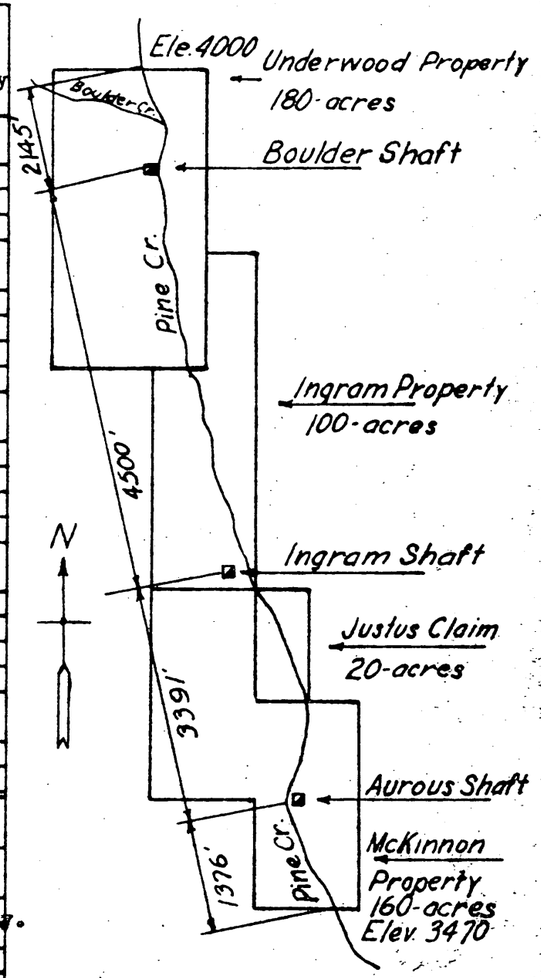

PINE CREEK OREGON, PLACER PROSPECTING

DATE ~~July 23~~ 1940

	Footage today	Footage To Date	Yardage Today	Yardage To Date	Number Samples	Average Recovery per Cu.Yd. To DATE.	Recovery Today	Recovery To Date	Assessment Work Today	Assessment Work To Date	Preparatory Today	Preparatory To Date
Boulder shaft												
Preparatory												
Sampling												
New Drifting				~~57.38~~	~~12~~	~~2.15~~		~~83.39~~				~~753.07~~
Ingram Shaft												
Preparatory												
Sampling												
New Drifting			~~5.78~~	~~24.00~~	~~8~~	~~8.56~~	~~16.75~~	~~57.06~~				~~972.81~~
Assessment Work												
Prospect Shaft No. 1										~~510.00~~		
Preparatory												
Sinking												
East drift												
West drift												
Prospect Shaft No. 2												
Preparatory												
Sinking												
East drift												
West drift												
Justus Claim												
Assessment Work										~~165.07~~		

	To Day	To Date
Personnel		
Pay Roll	~~10~~	
Mat. & Supplies (Approx.)	~~118.30~~	~~2749.14~~
Other Expense (Approx.)		~~675.45~~
	~~20.00~~	~~463.30~~
Total Expense (Approx.)	~~148.30~~	~~3865.49~~

Trend of Pine Creek:

Weather: ~~Clear & hot~~

Remarks:

~~Sampling is proceeding satisfactorily.~~

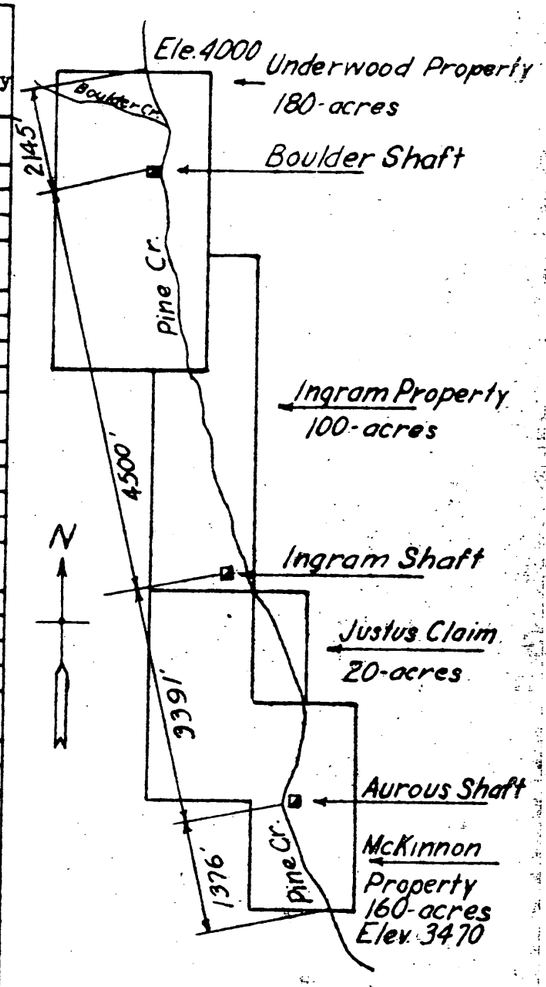

PINE CREEK OREGON, PLACER PROSPECTING

DATE Jul. 24 1940

	Footage today	Footage To Date	Yardage Today	Yardage To Date	Number Samples	Average Recovery per Cu.Yd. To Date	Recovery Today	Recovery To Date	Assessment Work Today	Assessment Work To Date	Preparatory Today	Preparatory To Date
Boulder shaft												
Preparatory												753.97
Sampling				57.[illegible]	12	[illegible].15		80.[illegible]				
New Drifting												
Ingram Shaft												
Preparatory												
Sampling												272.91
New Drifting			4.57	20.[illegible]	1	5.17	91.32	14[illegible].38				
Assessment Work												
										510.82		
Prospect Shaft No. 1												
Preparatory												
Sinking												
East drift												
West drift												
Prospect Shaft No. 2												
Preparatory												
Sinking												
East drift												
West drift												
Justus Claim												
Assessment Work												
										102.77		

	To Day	To Date
Personnel	20	
Pay Roll	128.85	2577.99
Mat. & Supplies (Approx.)	65.41	738.84
Other Expense (Approx.)	20.00	483.20
Total Expense (Approx.)	214.26	4100.03

Trend of Pine Creek:

Weather: Cloudy, cooler

Remarks: Sample to-day was taken in a section of the workings where it has been reported to us that good values were recovered. We feel that this sample verifies some of the verbal reports we have received from miners who worked in this shaft. There is no particular reason from the character of the bed rock or the formation of the gravel why this sample should have been so very good.

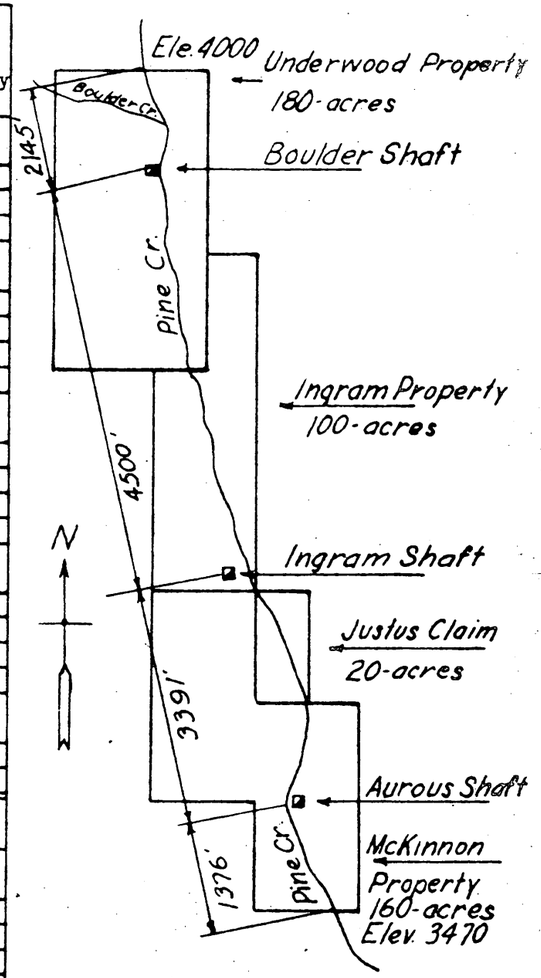

PINE CREEK OREGON, PLACER PROSPECTING

DATE July 25 1940

	Footage today	Footage To Date	Yardage Today	Yardage To Date	Number Samples	Average Recovery per Cu.Yd. to DATE.	Recovery Today	Recovery To Date	Assessment Work Today	Assessment Work To Date	Preparatory Today	Preparatory To Date
Boulder shaft												
Preparatory												753.97
Sampling				37.35	19	2.15		8 .39				
New Drifting												
Ingram Shaft												
Preparatory												
Sampling			6.13	43.17	2	4.24	28.04	170.48				972.91
New Drifting												
Assessment Work										510.82		
Prospect Shaft No. 1												
Preparatory												
Sinking												
East drift												
West drift												
Prospect Shaft No. 2												
Preparatory												
Sinking												
East drift												
West drift												
Justus Claim												
Assessment Work										103.77		

	To Day	To Date
Personnel	20	
Pay Roll	121.63	[illegible]
Mat. & Supplies (Approx.)		738.14
Other Expense (Approx.)	20.00	301.29
Total Expense (Approx.)	141.63	4[illegible]1.66

Trend of Pine Creek:

Weather: Cloudy and light showers at night.

Remarks: [illegible] weather large boulders encountered in both cross-cuts which required blasting.

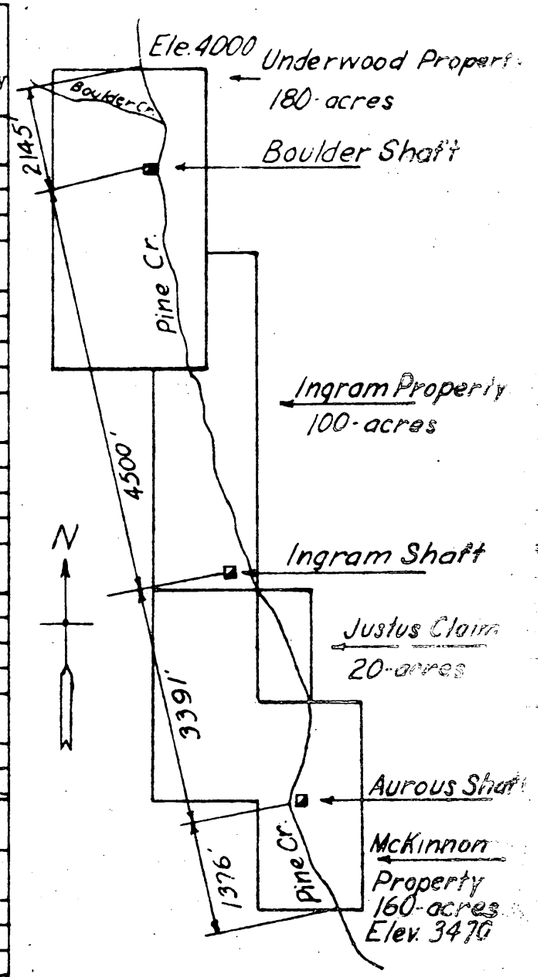

PINE CREEK OREGON, PLACER PROSPECTING

DATE July 28 1940

	Footage today	Footage To Date	Yardage Today	Yardage To Date	Number Samples	Average Recovery per Cu.Yd. To Date	Recovery Today	Recovery To Date	Assessment Work Today	Assessment Work To Date	Preparatory Today	Preparatory To Date
Boulder shaft												
Preparatory												756.32
Sampling				27.75	13	1.15		32.29				
New Drifting												
Ingram Shaft												
Preparatory												972.91
Sampling			4.4	23.71	1	4.65	18.07	162.49				
New Drifting												
Assessment Work										510.22		
Prospect Shaft No. 1												
Preparatory												
Sinking												
East drift												
West drift												
Prospect Shaft No. 2												
Preparatory												
Sinking												
East drift												
West drift												
Justus Claim												
Assessment Work										103.77		

	To Day	To Date
Personnel	20	
Pay Roll	120.31	1320.13
Mat. & Supplies (Approx.)	27.41	266.23
Other Expense (Approx.)	29.09	833.56
Total Expense (Approx.)	177.22	4419.53

Trend of Pine Creek:

Weather: Rain.

Remarks: [illegible]

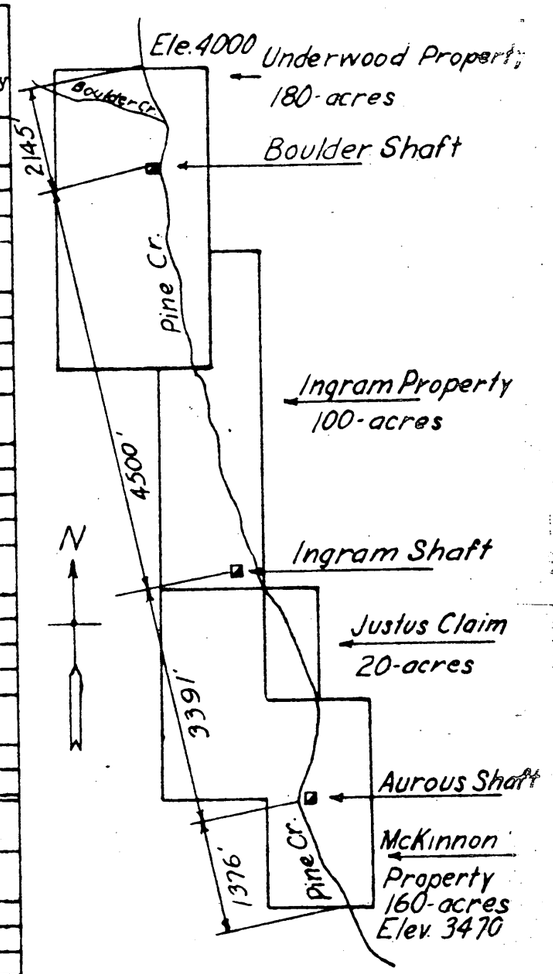

PINE CREEK OREGON, PLACER PROSPECTING

DATE July 27 1940

	Footage today	Footage To Date	Yardage Today	Yardage To Date	Number Samples	Average Recovery per Cu.Yd. TO DATE.	Recovery Today	Recovery To Date	Assessment Work Today	Assessment Work To Date	Preparatory Today	Preparatory To Date
Boulder shaft												
Preparatory												755.97
Sampling				37.35	19	2.15		80.39				
New Drifting												
Ingram Shaft												
Preparatory												
Sampling			22.21	21.43	3	4.77	53.00	845.49				578.31
New Drifting												
Assessment Work										510.32		
Prospect Shaft No. 1												
Preparatory												
Sinking												
East drift												
West drift												
Prospect Shaft No. 2												
Preparatory												
Sinking												
East drift												
West drift												
Justus Claim												
Assessment Work										103.77		

	To Day	To Date
Personnel	13	
Pay Roll	119.41	3543.54
Mat. & Supplies (Approx.)		766.25
Other Expense (Approx.)	20.00	643.20
Total Expense (Approx.)	139.41	4953.39

Trend of Pine Creek:

Weather: Cloudy and cooler

Remarks: Sampling progressing satisfactorily.

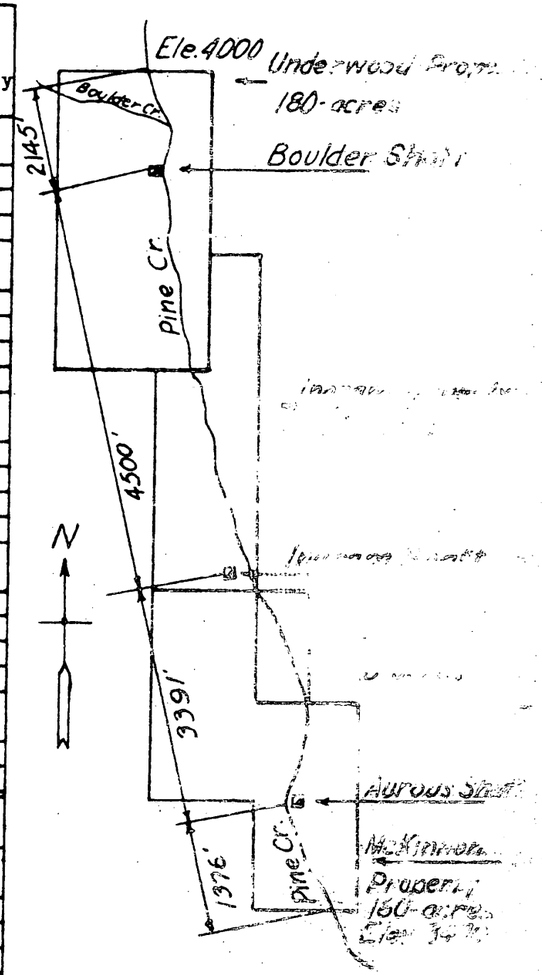

PINE CREEK OREGON, PLACER PROSPECTING

DATE July 28 1940

	Footage today	Footage To Date	Yardage Today	Yardage To Date	Number Samples	Average Recovery per Cu.Yd.	Recovery Today	Recovery To Date	Assessment Work Today	Assessment Work To Date	Preparatory Today	Preparatory To Date
Boulder shaft												
Preparatory												
Sampling												[illegible]
New Drifting				[illegible]	[illegible]	[illegible]		[illegible]				
Ingram Shaft												
Preparatory												
Sampling												[illegible]
New Drifting			[illegible]	[illegible]	1	4.56	[illegible]	[illegible]				
Assessment Work												
										510.92		
Prospect Shaft No. 1												
Preparatory												
Sinking												
East drift												
West drift												
Prospect Shaft No. 2												
Preparatory												
Sinking												
East drift												
West drift												
Justus Claim												
Assessment Work												
										103.27		

	To Day	To Date
Personnel	18	
Pay Roll	110.41	[illegible]
Mat. & Supplies (Approx.)		[illegible]
Other Expense (Approx.)	[illegible]	[illegible]
Total Expense (Approx.)	133.41	[illegible]

Trend of Pine Creek:

Weather: Rain and [illegible]

Remarks: It is reported that sampling will be completed in this shaft by [illegible] of this week.

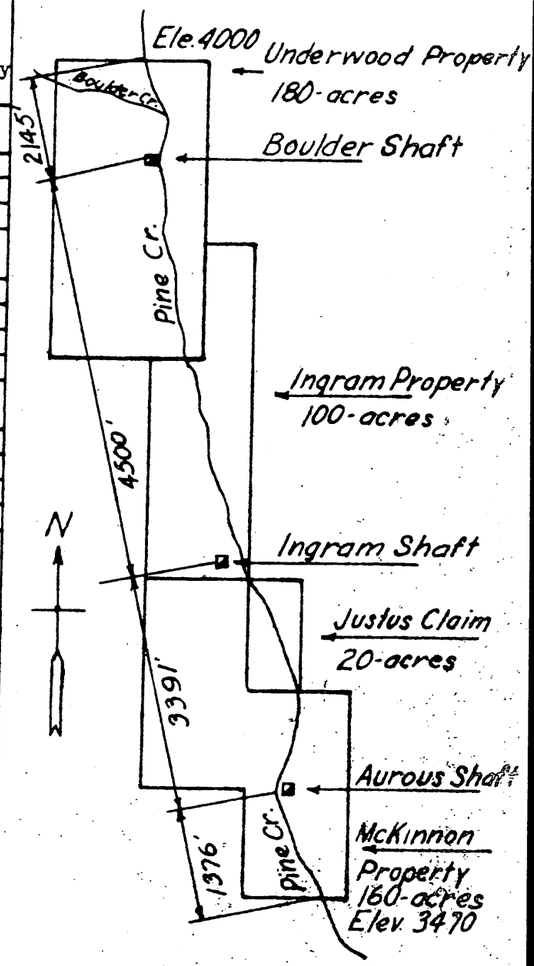

PINE CREEK OREGON, PLACER PROSPECTING

DATE July 29 1940

	Footage today	Footage To Date	Yardage Today	Yardage To Date	Number Samples	Average Recovery per Cu.Yd. TO DATE.	Recovery Today	Recovery To Date	Assessment Work Today	Assessment Work To Date	Preparatory Today	Preparatory To Date
Boulder shaft												
Preparatory												953.97
Sampling				37.38	19	2.15		80.39				
New Drifting												
Ingram Shaft												
Preparatory												972.91
Sampling			4.5	68.68	1	4.34	7.47	278.39				
New Drifting												
Assessment Work										510.82		
Prospect Shaft No. 1												
Preparatory												
Sinking												
East drift												
West drift												
Prospect Shaft No. 2												
Preparatory												
Sinking												
East drift												
West drift												
Justus Claim												
Assessment Work										103.77		

	To Day	To Date
Personnel	19	
Pay Roll	124.41	3493.58
Mat. & Supplies (Approx.)	112.77	879.02
Other Expense (Approx.)	30.00	593.28
Total Expense (Approx.)	267.18	4965.58

Trend of Pine Creek:

Weather: Fair and warm

Remarks: sampling progressing satisfactorily.

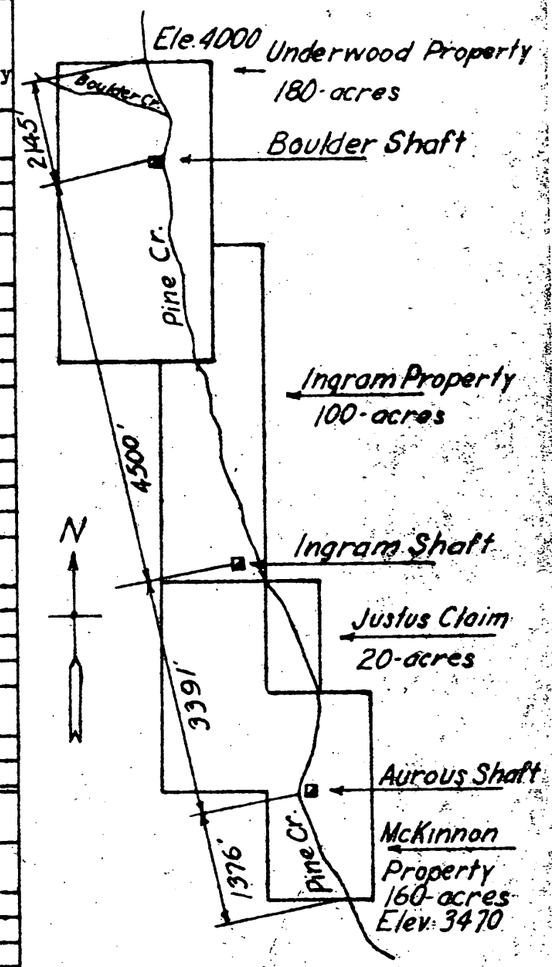

PINE CREEK OREGON, PLACER PROSPECTING

DATE July 30 1940

	Footage today	Footage To Date	Yardage Today	Yardage To Date	Number Samples	Average Recovery per Cu.Yd. TO DATE.	Recovery Today	Recovery To Date	Assessment Work Today	Assessment Work To Date	Preparatory Today	Preparatory To Date
Boulder shaft												
Preparatory												753.97
Sampling				37.35	19	2.15		80.39				
New Drifting												
Ingram Shaft												
Preparatory												
Sampling			7.25	69.91	1	4.14	17.47	289.35				972.91
New Drifting												
Assessment Work										510.32		
Prospect Shaft No. 1												
Preparatory												
Sinking												
East drift												
West drift												
Prospect Shaft No. 2												
Preparatory												
Sinking												
East drift												
West drift												
Justus Claim												
Assessment Work										103.77		

	To Day	To Date
Personnel	19	
Pay Roll	124.41	3617.77
Mat. & Supplies (Approx.)	5.05	822.01
Other Expense (Approx.)	30.00	523.26
Total Expense (Approx.)	157.46	5123.04

Trend of Pine Creek:

Weather: Rain in afternoon and evening.

Remarks:

Ground in east crosscut is decreasing in value and sampling will be discontinued in this area today

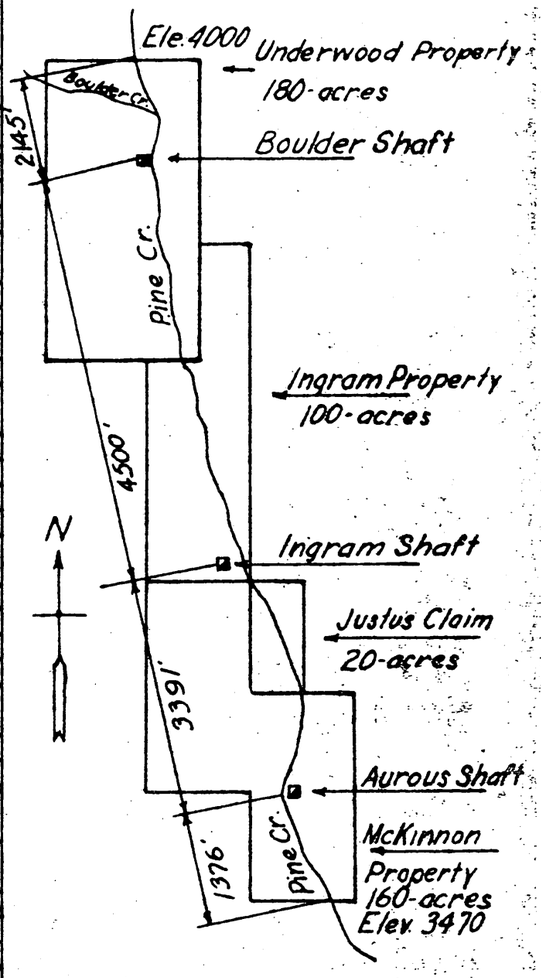

PINE CREEK OREGON, PLACER PROSPECTING

DATE July 31 1940

	Footage today	Footage To Date	Yardage Today	Yardage To Date	Number Samples	Average Recovery per Cu.Yd. TO DATE.	Recovery Today	Recovery To Date	Assess-ment Work Today	Assess-ment Work To Date	Preparatory Today	Preparatory To Date
Boulder shaft												
Preparatory												753.97
Sampling				37.35	19	2.15		80.39				
New Drifting												
Ingram Shaft												
Preparatory												
Sampling												872.91
[illegible] Drifting			8.8	23.21	2	3.90	17.60	307.46				
Assessment Work												
										510.82		
Prospect Shaft No. 1												
Preparatory												
Sinking												
East drift												
West drift												
Prospect Shaft No. 2												
Preparatory												
Sinking												
East drift												
West drift												
Justus Claim												
Assessment Work												
										103.77		

	To Day	To Date
Personnel	21	
Pay Roll	134.40	3752.17
Mat. & Supplies (Approx.)	17.18	899.19
Other Expense (Approx.)	30.00	653.20
Total Expense (Approx.)	181.52	5304.56

Trend of Fine Creek:

Weather: Fair and cooler

Remarks: To-morrow will complete sampling in the lower levels. We will then take samples at various stages coming up the shaft to determine the values in the top gravel.

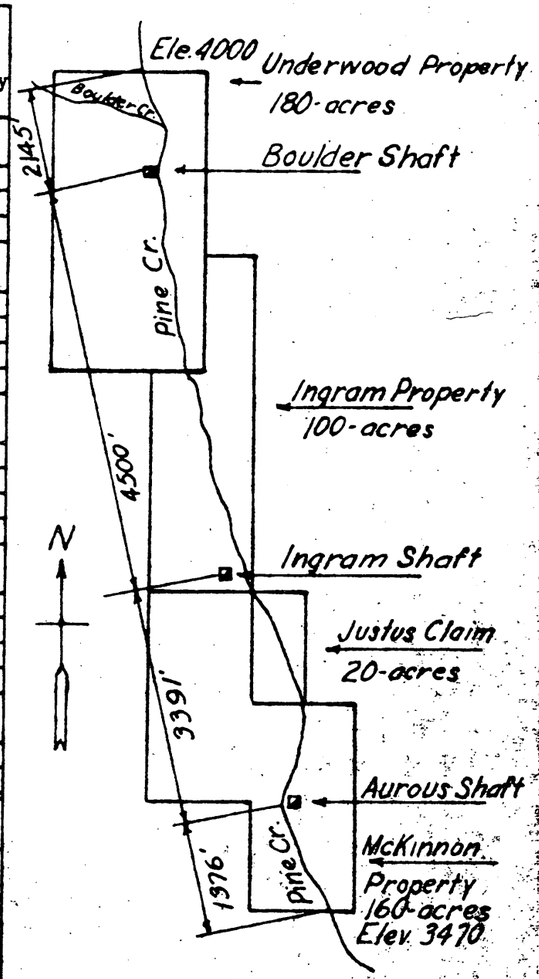

PINE CREEK OREGON, PLACER PROSPECTING

DATE Aug 1 1940

	Footage today	Footage To Date	Yardage Today	Yardage To Date	Number Samples	Average Recovery per Cu.Yd. TO DATE.	Recovery Today	Recovery To Date	Assessment Work Today	Assessment Work To Date	Preparatory Today	Preparatory To Date
Boulder shaft												~~853.07~~
Preparatory												
Sampling				37.35	19	2.15		80.39				
New Drifting												
Ingram Shaft												
Preparatory												~~972.01~~
Sampling			~~4.22~~	~~82.93~~	~~2~~	~~4.22~~	~~42.62~~	~~350.08~~				
New Drifting												
Assessment Work										~~510.68~~		
Prospect Shaft No. 1												
Preparatory												
Sinking												
East drift												
West drift												
Prospect Shaft No. 2												
Preparatory												
Sinking												
East drift												
West drift												
Justus Claim												
Assessment Work										~~103.77~~		

	To Day	To Date
Personnel	17	
Pay Roll	114.42	~~3866.58~~
Mat. & Supplies (Approx.)		~~899.19~~
Other Expense (Approx.)	~~10.00~~	~~663.20~~
Total Expense (Approx.)	~~124.42~~	~~5428.98~~

Trend of Pine Creek:

Remarks:

Weather: ~~Clear and Calm.~~

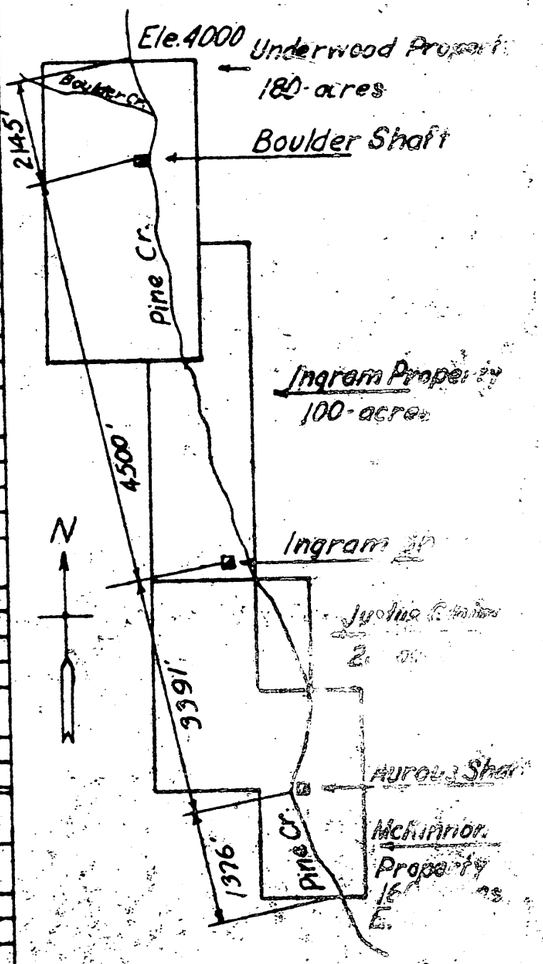

PINE CREEK OREGON, PLACER PROSPECTING

DATE Aug 2 1940

	Footage today	Footage To Date	Yardage Today	Yardage To Date	Number Samples	Average Recovery per Cu.Yd. TO DATE.	Recovery Today	Recovery To Date	Assess-ment Work Today	Assess-ment Work To Date	Preparatory Today	Preparatory To Date
Boulder shaft												
Preparatory												753.97
Sampling				37.35	19	2.15		80.39				
New Drifting												
Ingram Shaft												
Preparatory												
Sampling			2.89	85.82	1	4.60	45.40	395.48				972.91
New Drifting												
Assessment Work										510.82		
Prospect Shaft No. 1												
Preparatory												
Sinking												
East drift												
West drift												
Prospect Shaft No. 2												
Preparatory												
Sinking												
East drift												
West drift												
Justus Claim												
Assessment Work										103.77		

	To Day	To Date
Personnel	15	
Pay Roll	103.87	3970.45
Mat. & Supplies (Approx.)		899.12
Other Expense (Approx.)	10.00	673.28
Total Expense (Approx.)	113.87	5542.85

Trend of Pine Creek:

Weather: Fair and warm

Remarks:

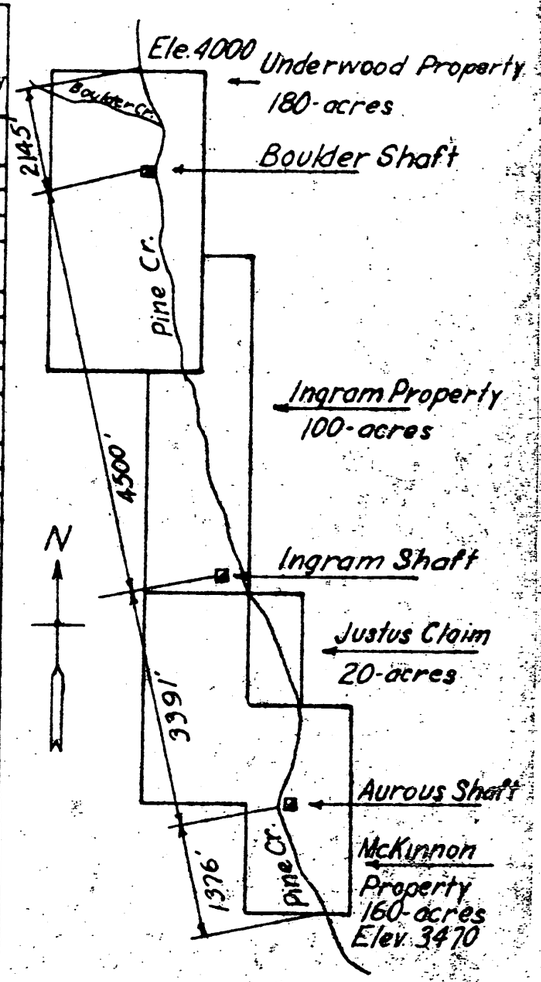

PINE CREEK OREGON, PLACER PROSPECTING

DATE Aug 3 1940

	Footage today	Footage To Date	Yardage Today	Yardage To Date	Number Samples	Average Recovery per Cu.Yd. TO DATE.	Recovery Today	Recovery To Date	Assessment Work Today	Assessment Work To Date	Preparatory Today	Preparatory To Date
Boulder shaft												
Preparatory												753.97
Sampling				37.35	19	2.15		80.39				
New Drifting												
Ingram Shaft												
Preparatory												972.91
Sampling				85.82	25	4.60		395.48				
New Drifting												
Assessment Work										510.82		
Prospect Shaft No. 1												
Preparatory												
Sinking												
East drift												
West drift												
Prospect Shaft No. 2												
Preparatory												
Sinking												
East drift												
West drift												
Justus Claim												
Assessment Work										103.97		

	To Day	To Date
Personnel	14	
Pay Roll	97.77	4063.33
Mat. & Supplies (Approx.)		899.19
Other Expense (Approx.)	10.00	685.80
Total Expense (Approx.)	107.77	5650.68

Trend of Pine Creek:

Weather: Fair and warm

Remarks:

This concludes sampling in both shafts. Plans and estimates for the layout and operation of this work - if carried further - are now being made and meeting will be held at an early date to determine if we will continue on with the work.
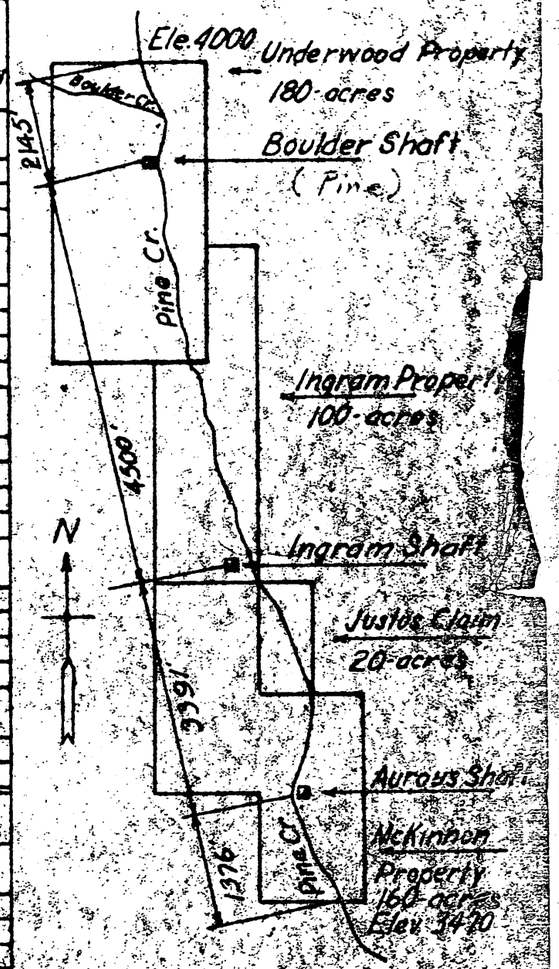
Shaft samples are not included in bedrock recovery yardage.
