DEFENSE MINERALS EXPLORATION ADMINISTRATION
CONTRACT ADMINISTRATION AND AUDIT DIVISION

REPORT OF REVIEW

I have reviewed the Monthly Reports of:

Hugh M. Simmons
801 Alhambra Boulevard
Sacramento, California

pertaining to Exploration Project Contract No. Idm-E829, Docket No. DMEA-3698, including Amendment No. 1, for the months of July 1955 to May 1956, inclusive, covering a project for the exploration of mercury, on property, known as the Granada Quicksilver Mine, located in Napa County, California.

My review included an examination of the Monthly Reports (Forms MF-104) and supporting documents attached thereto, comparison of the costs claimed with the contract and pertinent schedules, consultation with Excutive Officer in charge of the project, and a determination of the reasonableness and propriety of the costs.

This review was made in lieu of a final audit of the Operator's accounts and records for the following reason:

> All of the costs incurred were under a contract provision for payment by the Government on the basis of fixed unit costs of units of work actually performed.

The review disclosed the following facts in regard to the amount paid or to be paid the contractor.

Total cost as billed by contractor	$11,174.00
Exceptions	-0-
Total Accepted Cost	$11,174.00

The contract calls for a 75% participation of exploration expenses by the United States Government. Therefore, payment to the contractor by the Government in the amount of Eight Thousand Three Hundred Eighty and 50/100 Dollars:

** $8,380.50 **

is considered valid and proper, provided the Regional Executive Officer, the Administrator, or other competent official has accepted or will accept the project as having otherwise met the terms of the contract.

George Mavor
George Mavor
Auditor

September 18, 1956

UNITED STATES
DEPARTMENT OF THE INTERIOR
DEFENSE MINERALS EXPLORATION ADMINISTRATION
WASHINGTON 25, D. C.

RECEIVED
JUL 19 1956

420 Custom House
555 Battery Street
San Francisco 11, California

July 17, 1956

Air Mail

Mr. Jay L. Chambers, Chief
Contract Administration and Audit Division
Defense Mineral Exploration Administration
Washington 25, D. C.

Re: Idm-E829, DMEA-3698
Hugh M. Simmons
Granada Quicksilver Mine

Dear Mr. Chambers:

Reference is made to your letter dated July 11, 1956, in connection with submitting Report of Review for subject contract.

A Final claim for work performed under this contract has not as yet been submitted by the operator. Under date of April 23, 1956, Mr. S. Ricker advised the operator that the Government would not participate in more than 278 feet of drifting and crosscutting under Stage II as set forth under Exhibit "A" of the contract. The last MF-104 received from the operator was for three months ending February 29, 1956, and Form MF-104a showed a total of 172 feet of drifting and crosscutting, therefore the difference between the footage claimed for drifting and crosscutting and the footage of 278 feet authorized by Mr. Ricker is 106 feet. Interim Inspection Report dated April 18, 1956, parepared by D. B. Tatlock and E. H. Bailey, USGS, reported a total of 247 feet for drifting and crosscutting as of April 12, 1956.

Mr. S. Ricker advised me that Dr. Hugh M. Simmons, was on his vacation and would not return until sometime in August, and that the final drifting and crosscutting footage claim, could not be determined until the Examining Engineer had a chance to discuss the final claim with the operator.

It will be necessary to wait for the results of the above mentioned

conference, before submitting a Report of Review, and when all information has been received covering the final claim, a Report of Review will be forwarded promptly.

Sincerely yours,

George Mavor

George Mavor, Auditor

Copy to: S. Ricker

UNITED STATES
DEPARTMENT OF THE INTERIOR
DEFENSE MINERALS EXPLORATION ADMINISTRATION
WASHINGTON 25, D. C.

JUL 11 1956

Mr. George Mayer
DMEA Auditor
420 Custom House
555 Battery Street
San Francisco 11, California

Re: Docket No. DMEA-3698 (Mercury)
Hugh M. Simmons
Grenada Quicksilver Mine
Napa County, California
Contract No. Idm-K829

Dear Mr. Mayer:

This Division has been requested to complete the audit review of the referenced project as soon as possible.

I understand that this project was completed during the month of April 1956, and, since the contract is on the Short Form, it appears that a Report of Review may now be made. Please prepare and submit the report at your earliest opportunity.

Sincerely yours,

(Signed) J. L. Chambers

Jay L. Chambers, Chief
Contract Administration
and Audit Division

EDTalbert/wb
July 11, 1956

Copy to: Docket
Admr. Reading File
Mr. Martin
Mr. Chambers

Form MF-104 (Rev.)
(April 1952)

Budget Bureau No. 42-R1036.5

UNITED STATES
DEPARTMENT OF THE INTERIOR
DEFENSE MINERALS EXPLORATION ADMINISTRATION

RECEIVED SEP 27 1956

OPERATOR'S MONTHLY REPORT AND VOUCHER

Month of Mar., Apr., and May, 1956 Docket No. DMEA 3698 Contract No. Idm-E 829

Operator's Name Hugh M. Simmons Minerals

Address 801 Alhambra Blvd., Sacramento, Calif.

Contract Amount, $ 17,800.00 Government Participation: 75 % Amount, $ 13,350.00

ITEMS OF COSTS	FOR OPERATOR'S USE			FOR GOVERNMENT USE ONLY		
	Monthly Total	Totals Previously Reported	Totals To Date	Approved Monthly Total	Approved Totals Previously Reported	Approved Totals To Date
(1) Independent / Short Form Contracts:						
Drilling						
~~Bulldozing~~ Stage II:						
Crosscutting & Drifting	$3180.00	$5160.00	$8340.00			
~~Drifting~~ Timbering	28.00	406.00	434.00			
tage I: Rehabilitation	-	2400.00	2400.00			
(2) Labor and Supervision:						
Labor						
Supervision						
Technical Services						
(3) Operating Mat'ls. and Supplies:						
Timber						
Explosives						
Pipe						
Track						
(4) Operating Equipment:						
Rental						
Purchase						
Depreciation						
(5) Initial Rehabilitation and Repairs						
(6) New Bldgs., Improvements, etc.						
(7) Miscellaneous:						
Repairs to Equipment						
Sampling and Analysis						
Payroll Taxes						
Liability Insurance						
(8) Contingencies (specify):						
TOTALS	$3,208.00	$7966.00	$11,174.00			

I certify that the above bill is correct and just and that payment therefor has not been received.

Date Aug. 7, 1956 *Payee Hugh M. Simmons

Per _____ Title Owner

*When a voucher is signed or receipted in the name of a company or corporation, the name of the person writing the company or corporate name, as well as the capacity in which he signs, must appear. For example: "John Doe Company, per John Smith, Secretary," or "Treasurer," as the case may be.

NOTE.—Title 18, U. S. Code (Crimes), section 1001, makes it a criminal offense to make a willfully false statement or representation to any department or agency of the United States as to any matter within its jurisdiction.

(Instructions on reverse)

Pursuant to authority vested in me, I certify that this account is correct and proper for payment in the amount of:

$ 2406 00

Lloyd W. Sjolander
Authorized Certifying Officer

Signature _____ (Authorized Certifying Officer)

Date SEP 24 1956 Vou. No. SF-DMEA-9

(See other side)

(For Government use only)

CERTIFICATION BY GOVERNMENT REPRESENTATIVE:

I certify that to the best of my knowledge and belief the contractor submitting this voucher is operating a Defense Minerals Exploration Administration project under Contract No. IdM E829 in accordance with the terms of the contract.

Signature John Stone Title Mining Engineer Date 8/8/56

APPROVAL BY DMEA EXECUTIVE OFFICER OR ALTERNATE:

Signature [illegible] Title Executive Officer Date 8/8/56

MONTHLY REPORT OF OPERATOR

The Operator (Contractor) of an exploration project is required to make a monthly report to the Government through the Regional Executive Officer. This report consists of three parts as follows:

(a) *Form MF-104—Operator's Monthly Report and Voucher.*—This form details expenditures and constitutes a voucher for reimbursing the Operator for the Government's share of costs;

(b) *Form MF-104A—Operator's Unit Cost and Progress Report.*—This is a statistical report of expenditures which shows costs for the various types of operation; and

(c) *Narrative.*—A concise narrative description of progress made, results accomplished, and any unusual difficulties encountered must be furnished as an attachment to this Report and Voucher. Wherever possible, the narrative is to be illustrated with maps or sketches showing formations penetrated and location and assays of samples taken as well as advances in workings. In the case of diamond drilling or churn drilling, the location and inclination of holes is to be shown on a map; logs and assays also are to be submitted.

The Monthly Report of Operator should be prepared in an original and four copies all of which must be sent to the Executive Officer of the Region not later than the 15th of the month following.

Preparation of Form MF-104—Operator's Monthly Report and Voucher.—All the applicable spaces in Form MF-104 should be filled in by the Operator, and the Operator or his agent should sign the certification in the lower left corner of the form.

The items of costs are arranged in the order they appear in Article 6 (a) of Form MF-200 (Revised February 1952), however, this form is readily adaptable for use in reporting activities under other contract forms.

Under Item (1) delete words "Short Form" if the contract is a sub-contract under Form MF-200; and delete word "Independent" if the contract reported is on Form MF-200 (A). Also, report work paid for on a unit basis under contract Form MF-200 as though it were performed under an independent contract.

Under Item (2) include labor, supervision and technical services incurred for the exploratory operations. Do not include labor, supervision and technical services used for work performed under items (5) and (6).

Under Item (3) include the costs of material and supplies used in the project other than that used under items (5) and (6).

Under Item (4) appear the three types of operating equipment expenditures, that is, rental, purchase and depreciation. The expenditures made for renting equipment belonging to a third party will be reported under "Rental". The amount paid or duly obligated for payment for the purchase of equipment will be reported under "Purchase". The amount of expenditures due the Operator to reimburse him for depreciation of equipment owned will be reported under "Depreciation".

Item (5) comprises costs of labor, supervision, technical services, materials, etc., which are used in the initial rehabilitation and repair of existing buildings, installations, fixtures, and equipment. These costs, therefore, should not be reported under items (2) and (3).

Item (6) includes the labor, supervision, technical services, materials, etc., used in the installation or construction of new buildings, fixed improvements, etc., necessary for the project. These costs, therefore, should not be reported under items (2) and (3).

Item (7) covers miscellaneous types of expenditure such as payroll taxes, liability insurance, workmen's compensation insurance, repairs to equipment and sampling and analysis. Only that part of payroll taxes, liability insurance and workmen's compensation which are paid by the operator should be reported under item (7). The share paid by the employee as a payroll deduction is to be included under item (2) as labor costs.

Item (8) includes any unforeseen costs not included in the other seven categories.

The original of Form MF-104 when submitted for reimbursable expenses incurred under contract Form MF-200 must be supported by original documentation or by certified copies of purchase orders, payrolls or transcripts of payrolls, unless such documentation has been waived by the Regional Executive Officer. This certification may be stated thus, "Certified True Copy (or Transcript)", followed by appropriate signature. If the Executive Officer of the Region determines that a contract under Form MF-200 should have an "on-site" audit, that is, a Government auditor should make an audit of the Operator's books and records of account, the Operator need not support his monthly voucher with original or certified documents except in cases of equipment purchases whose individual costs exceed $50.00. In these cases the original or a certified copy of the purchase order or invoice should be attached to the Monthly Voucher. N. B.—Only the *original* of Form MF-104 is required to be documented. The four copies of Form MF-104 are not to be thus supported.

Form MF-104 submitted for reimbursement under fixed price contracts on Form MF-200 (A), however, are not required to be supported by documentation of any kind. The Operator will submit his claim under item (1) of Form MF-104 by deleting as stated above the word "Independent" and by showing the number of feet or other units immediately after the appropriate descriptive word, such as, drilling, bulldozing, crosscutting, drifting, etc., and giving the "Monthly Total" amount due. "Totals Previously Reported", and "Totals to Date" columns should also be filled in.

GPO 872893

Form MF-104A
(April 1952)

Budget Bureau No. 42-R1151.2

UNITED STATES
DEPARTMENT OF THE INTERIOR

DEFENSE MINERALS EXPLORATION ADMINISTRATION

OPERATOR'S UNIT COST AND PROGRESS REPORT

RECEIVED
SEP 27 1956

Month of Mar., Apr., and May 1956 Docket No. DMEA 3698 Contract No. Idm-E 829
Operator's Name Hugh M. Simmons Minerals Mercury
Address 801 Alhambra Boulevard, Sacramento, Calif.

OPERATION	UNIT	COSTS THIS MONTH	UNITS THIS MONTH	COSTS TO DATE	UNITS TO DATE	UNIT COSTS TO DATE	AUTHORIZED BY CONTRACT Units	AUTHORIZED BY CONTRACT Unit Costs
Stage II								
Drifting and crosscutting	Ft.	$3180.00	106	$8340.00	278	30.00	440	$30.00
Crosscutting								
Raising								
~~Shafts~~ Timbering	Ft.	28.00	4	434.00	62	7.00	300	7.00
Winzes								
Drilling: Core								
Churn								
Auger								
Stage I								
~~Trenching~~ Rehabilitation	Ft.	-	-	2400.00	200	12.00	200	12.00
~~Test Pits~~ Sample analysis	Ca	-	-	-	-	-	20	2.00
Roads and Trails								
TOTAL DISTRIBUTED COSTS		$3208.00	-	$11,174.00				TOTAL COSTS AUTHORIZED BY CONTRACT
Operating Equipment Purchased							Stage I	$2400.00
Initial Rehabilitation and Repairs							Stage II	15,360.00
New Buildings, Improvements, etc.								
TOTAL COSTS								$17,800.00

The undersigned company, and the official executing this certification on its behalf, hereby certify that the information contained in this report is correct and complete to the best of their knowledge and belief.

Date Aug. 7, 1956 Operator Hugh M. Simmons
Hugh M. Simmons
Per Title Owner

REMARKS:

NOTE.—Title 18, U. S. Code (Crimes), section 1001, makes it a criminal offense to make a willfully false statement or representation to any department or agency of the United States as to any matter within its jurisdiction.

(Instructions on reverse)

(For Government use only)

John S. Maine

INSTRUCTIONS

Preparation of Form MF-104A—Operator's Unit Cost and Progress Report.—Applicable places on Form 104A should be filled in by the Operator. The purpose of this form is twofold as follows: (1) to furnish the supervising engineers and other administrators with statistical information necessary to better determine the progress of the project; and (2) to furnish more permanent information on mining costs for future use. The more important phases of operation on which permanent information is desired have been outlined in the form. There are blank lines, however, for those unusual phases which may need to be reported for a particular project. It will be necessary for the Operator to distribute his costs among the applicable phases reported with the exception of three items the costs of which are not to be distributed by the Operator. These three items are: "Operating Equipment Purchased", "Initial Rehabilitation and Repairs", and "New Buildings, Improvements, etc." The reason for not distributing these items on a monthly basis is doubtless clear to the Operator, since such distribution might well overstate the cost for any one month or period short of the entire contract period.

Form MF-104A has been designed to tie in with Form MF-104 for both monthly and cumulative costs. The "Total Costs" on Form MF-104A for each month should equal the monthly "Total Costs" as reported on Form MF-104. This is also true of the "Total Costs To Date".

In preparing Form MF-104A, it will be necessary frequently to distribute certain costs over a number of items. For instance, supervisory and engineering costs may have to be distributed over several phases, such as, drifting, crosscutting, raising, etc., provided that these items were reported active for the month. Such distributions should be made on the basis of time spent on the various phases, on man days of labor charged to such phases, or on some other equitable basis. "Operating Equipment", "Initial Rehabilitation and Repairs", and "New Buildings Improvements, etc.", will be distributed to the several phases of the project by the Washington Office of DMEA at the close of the project if determined necessary. The last two columns headed "Authorized by Contract" will be filled in by the Operator if such information is found in the contract. This information is usually a part of Exhibit "A" of the contract. A space for remarks has been provided for the use of the Operator to call attention to any unusual circumstances causing excessive or disproportionate unit costs.

GPO 872894

RECEIVED
SEP 27 1956

NARRATIVE REPORT

A total of 106 feet of drifting and four feet of timbering were completed during the period.

Some cinnabar mineralization was encountered at the 240-foot point in the lower adit drift.

Several long holes have been drilled on the operator's account to check for mineralization away from the drift.

Further exploration is planned in the lower adit level.

Hugh M. Simmons

Hugh M. Simmons

Form MF-104 (Rev.)
(April 1952)

Budget Bureau No. 42-R1036.5

UNITED STATES
DEPARTMENT OF THE INTERIOR
DEFENSE MINERALS EXPLORATION ADMINISTRATION

OPERATOR'S MONTHLY REPORT AND VOUCHER

RECEIVED MAR 6 1956

Month of ~~Jan~~ Dec 1955 ~~Feb~~, 195~~6~~ Docket No. DMEA 3698 Contract No. Idm E 820

Operator's Name Hugh F. Simmons Minerals Mercury

Address 801 Alhambra Blvd Sacramento, Calif.

Contract Amount, $ 17,000.00 Government Participation: 75 % Amount, $ 13,350.00

ITEMS OF COSTS	FOR OPERATOR'S USE: Monthly Total	Totals Previously Reported	Totals To Date	FOR GOVERNMENT USE ONLY: Approved Monthly Total	Approved Totals Previously Reported	Approved Totals To Date
(1) Independent Short Form Contracts:						
Drilling						
Bulldozing						
Crosscutting & Drifting	2700.00	2,460.00	5,160.00			
~~Drifting~~ ~~xxxx~~ Timbering	210.00	196.00	400.00			
Stage 1 Rehabilitation		2,400.00	2,400.00			
(2) Labor and Supervision:						
Labor						
Supervision						
Technical Services						
(3) Operating Mat'ls. and Supplies:						
Timber						
Explosives						
Pipe						
Track						
(4) Operating Equipment:						
Rental						
Purchase						
Depreciation						
(5) Initial Rehabilitation and Repairs						
(6) New Bldgs., Improvements, etc.						
(7) Miscellaneous:						
Repairs to Equipment						
Sampling and Analysis						
Payroll Taxes						
Liability Insurance						
(8) Contingencies (specify):						
TOTALS	$2,910.00	5,056.00	7,960.00			

I certify that the above bill is correct and just and that payment therefor has not been received.

Date 24 Feb 56 *Payee Hugh F. Simmons

Per Hugh F. Simmons, M. D. Title Owner

*When a voucher is signed or receipted in the name of a company or corporation, the name of the person writing the company or corporate name, as well as the capacity in which he signs, must appear. For example: "John Doe Company, per John Smith, Secretary," or "Treasurer," as the case may be.

NOTE.—Title 18, U. S. Code (Crimes), section 1001, makes it a criminal offense to make a willfully false statement or representation to any department or agency of the United States as to any matter within its jurisdiction.

(Instructions on reverse)

Pursuant to authority vested in me, I certify that this account is correct and proper for payment in the amount of:

$ 2182.50

Signature
(Authorized Certifying Officer)

Date MAR 20 1956 Vou. No. SF-DMCA-30

(See other side)

(For Government use only)

CERTIFICATION BY GOVERNMENT REPRESENTATIVE:

I certify that to the best of my knowledge and belief the contractor submitting this voucher is operating a Defense Minerals Exploration Administration project under Contract No. Idm-E829 in accordance with the terms of the contract.

Signature John D. Warne Title Mining Engineer Date 3/2/56

John D. Warne

APPROVAL BY DMEA EXECUTIVE OFFICER OR ALTERNATE:

Signature S. Ricker Title Executive Officer Date 3/2/56

S. Ricker

MONTHLY REPORT OF OPERATOR

The Operator (Contractor) of an exploration project is required to make a monthly report to the Government through the Regional Executive Officer. This report consists of three parts as follows:

(a) *Form MF-104—Operator's Monthly Report and Voucher.*—This form details expenditures and constitutes a voucher for reimbursing the Operator for the Government's share of costs;

(b) *Form MF-104A—Operator's Unit Cost and Progress Report.*—This is a statistical report of expenditures which shows costs for the various types of operation; and

(c) *Narrative.*—A concise narrative description of progress made, results accomplished, and any unusual difficulties encountered must be furnished as an attachment to this Report and Voucher. Wherever possible, the narrative is to be illustrated with maps or sketches showing formations penetrated and location and assays of samples taken as well as advances in workings. In the case of diamond drilling or churn drilling, the location and inclination of holes is to be shown on a map; logs and assays also are to be submitted.

The Monthly Report of Operator should be prepared in an original and four copies all of which must be sent to the Executive Officer of the Region not later than the 15th of the month following.

Preparation of Form MF-104—Operator's Monthly Report and Voucher.—All the applicable spaces in Form MF-104 should be filled in by the Operator, and the Operator or his agent should sign the certification in the lower left corner of the form.

The items of costs are arranged in the order they appear in Article 6 (a) of Form MF-200 (Revised February 1952), however, this form is readily adaptable for use in reporting activities under other contract forms.

Under Item (1) delete words "Short Form" if the contract is a sub-contract under Form MF-200; and delete word "Independent" if the contract reported is on Form MF-200 (A). Also, report work paid for on a unit basis under contract Form MF-200 as though it were performed under an independent contract.

Under Item (2) include labor, supervision and technical services incurred for the exploratory operations. Do not include labor, supervision and technical services used for work performed under items (5) and (6).

Under Item (3) include the costs of material and supplies used in the project other than that used under items (5) and (6).

Under Item (4) appear the three types of operating equipment expenditures, that is, rental, purchase and depreciation. The expenditures made for renting equipment belonging to a third party will be reported under "Rental". The amount paid or duly obligated for payment for the purchase of equipment will be reported under "Purchase". The amount of expenditures due the Operator to reimburse him for depreciation of equipment owned will be reported under "Depreciation".

Item (5) comprises costs of labor, supervision, technical services, materials, etc., which are used in the initial rehabilitation and repair of existing buildings, installations, fixtures, and equipment. These costs, therefore, should not be reported under items (2) and (3).

Item (6) includes the labor, supervision, technical services, materials, etc., used in the installation or construction of new buildings, fixed improvements, etc., necessary for the project. These costs, therefore, should not be reported under items (2) and (3).

Item (7) covers miscellaneous types of expenditure such as payroll taxes, liability insurance, workmen's compensation insurance, repairs to equipment and sampling and analysis. Only that part of payroll taxes, liability insurance and workmen's compensation which are paid by the operator should be reported under item (7). The share paid by the employee as a payroll deduction is to be included under item (2) as labor costs.

Item (8) includes any unforeseen costs not included in the other seven categories.

The original of Form MF-104 when submitted for reimbursable expenses incurred under contract Form MF-200 must be supported by original documentation or by certified copies of purchase orders, payrolls or transcripts of payrolls, unless such documentation has been waived by the Regional Executive Officer. This certification may be stated thus, "Certified True Copy (or Transcript)", followed by appropriate signature. If the Executive Officer of the Region determines that a contract under Form MF-200 should have an "on-site" audit, that is, a Government auditor should make an audit of the Operator's books and records of account, the Operator need not support his monthly voucher with original or certified documents except in cases of equipment purchases whose individual costs exceed $50.00. In these cases the original or a certified copy of the purchase order or invoice should be attached to the Monthly Voucher. N. B.—Only the *original* of Form MF-104 is required to be documented. The four copies of Form MF-104 are not to be thus supported.

Form MF-104 submitted for reimbursement under fixed price contracts on Form MF-200 (A), however, are not required to be supported by documentation of any kind. The Operator will submit his claim under item (1) of Form MF-104 by deleting as stated above the word "Independent" and by showing the number of feet or other units immediately after the appropriate descriptive word, such as, drilling, bulldozing, crosscutting, drifting, etc., and giving the "Monthly Total" amount due. "Totals Previously Reported", and "Totals to Date" columns should also be filled in.

Form MF-104A
(April 1952)

Budget Bureau No. 42-R1151.2

UNITED STATES
DEPARTMENT OF THE INTERIOR

DEFENSE MINERALS EXPLORATION ADMINISTRATION

RECEIVED
MAR 8 1956

OPERATOR'S UNIT COST AND PROGRESS REPORT

Month of ~~Jan.~~ December 1955, Feb. 1956 — Docket No. DMEA 3698 — Contract No. Tom 2829

Operator's Name Hugh M. Simmons — Minerals Mercury

Address 801 Alhambra Blvd. Sacramento, Calif.

OPERATION	Unit	Costs This Month	Units This Month	Costs to Date	Units to Date	Unit Costs to Date	Authorized by Contract: Units	Authorized by Contract: Unit Costs
STAGE 11								
Drifting & X-cutting	Ft.	2,700	90	5,160.00	172	30.00	440	30.00
Crosscutting								
Raising								
Shafts Timbering	Ft.	210	30	400.00	58	7.00	300	7.00
Winzes								
Drilling: Core								
Churn								
Auger								
Stripping								
Trenching								
Test Pits								
Roads and Trails								
Total Distributed Costs		$ 2,910.		5,560.00				
Operating Equipment Purchased								
Initial Rehabilitation and Repairs								
New Buildings, Improvements, etc.								
Total Costs								

Total Costs Authorized by Contract	
STAGE 1	$ 2,440.00
STAGE 11	15,360.00
	$ 17,800.00

The undersigned company, and the official executing this certification on its behalf, hereby certify that the information contained in this report is correct and complete to the best of their knowledge and belief.

Date 24 Feb 56 — Operator Hugh M. Simmons

Per _____ Title Owner

Remarks:

NOTE.—Title 18, U. S. Code (Crimes), section 1001, makes it a criminal offense to make a willfully false statement or representation to any department or agency of the United States as to any matter within its jurisdiction.

(Instructions on reverse)

(For Government use only) John D. Wasne

INSTRUCTIONS

Preparation of Form MF–104A—Operator's Unit Cost and Progress Report.—Applicable places on Form 104A should be filled in by the Operator. The purpose of this form is twofold as follows: (1) to furnish the supervising engineers and other administrators with statistical information necessary to better determine the progress of the project; and (2) to furnish more permanent information on mining costs for future use. The more important phases of operation on which permanent information is desired have been outlined in the form. There are blank lines, however, for those unusual phases which may need to be reported for a particular project. It will be necessary for the Operator to distribute his costs among the applicable phases reported with the exception of three items the costs of which are not to be distributed by the Operator. These three items are: "Operating Equipment Purchased", "Initial Rehabilitation and Repairs", and "New Buildings, Improvements, etc." The reason for not distributing these items on a monthly basis is doubtless clear to the Operator, since such distribution might well overstate the cost for any one month or period short of the entire contract period.

Form MF–104A has been designed to tie in with Form MF–104 for both monthly and cumulative costs. The "Total Costs" on Form MF–104A for each month should equal the monthly "Total Costs" as reported on Form MF–104. This is also true of the "Total Costs To Date".

In preparing Form MF–104A, it will be necessary frequently to distribute certain costs over a number of items. For instance, supervisory and engineering costs may have to be distributed over several phases, such as, drifting, crosscutting, raising, etc., provided that these items were reported active for the month. Such distributions should be made on the basis of time spent on the various phases, on man days of labor charged to such phases, or on some other equitable basis. "Operating Equipment", "Initial Rehabilitation and Repairs", and "New Buildings Improvements, etc.", will be distributed to the several phases of the project by the Washington Office of DMEA at the close of the project if determined necessary. The last two columns headed "Authorized by Contract" will be filled in by the Operator if such information is found in the contract. This information is usually a part of Exhibit "A" of the contract. A space for remarks has been provided for the use of the Operator to call attention to any unusual circumstances causing excessive or disproportionate unit costs.

GPO 872894

NARRATIVE REPORT

Ninety feet of drifting has been completed. Work has been delayed owing to severe storms and impassable roads. Slight mineralization has been encountered and car samples have been taken and are being held for your engineer. We will advise you when roads are passable so that an inspection can be made by your engineer.

We have done 250 feet of long hole drilling at our expense and good indication of cinnabar has been struck 42 feet east of face of drift. A heavy coarse stringer has been encountered which we believe is on the footwall of the mineralized zone.

Hugh M. Simmons M.D.

Hugh M. Simmons

Form MF-104 (Rev.)
(April 1952)

Budget Bureau No. 42-R1036.5

RECEIVED
DEC 23 1955

UNITED STATES
DEPARTMENT OF THE INTERIOR
DEFENSE MINERALS EXPLORATION ADMINISTRATION
OPERATOR'S MONTHLY REPORT AND VOUCHER

Month of Sept., Oct., Nov. 1955 Docket No. DMEA 3698 Contract No. Idm-E829
Operator's Name Hugh M. Simmons Minerals Mercury
Address 801 Alhambra Blvd., Sacramento, Calif.
Contract Amount, $17,800.00 Government Participation: 75 % Amount, $13,350.00

ITEMS OF COSTS	FOR OPERATOR'S USE			FOR GOVERNMENT USE ONLY		
	Monthly Total	Totals Previously Reported	Totals To Date	Approved Monthly Total	Approved Totals Previously Reported	Approved Totals To Date
Stage II:						
(1) ~~Independent~~ ~~Short Term~~ Contracts:						
Drilling						
Bulldozing						
Crosscutting & drifting	2,460	-	2,460.00			
~~Drifting~~ Timbering	196	-	196.00			
Stage I: Rehabilitation	-	2,400.00	2,400.00			
(2) Labor and Supervision:						
Labor						
Supervision						
Technical Services						
(3) Operating Mat'ls. and Supplies:						
Timber						
Explosives						
Pipe						
Track						
(4) Operating Equipment:						
Rental						
Purchase						
Depreciation						
(5) Initial Rehabilitation and Repairs						
(6) New Bldgs., Improvements, etc.						
(7) Miscellaneous:						
Repairs to Equipment						
Sampling and Analysis	-	-	-			
Payroll Taxes						
Liability Insurance						
(8) Contingencies (specify):						
TOTALS	2,656	2,400.00	5,056.00			

I certify that the above bill is correct and just and that payment therefor has not been received.

Date 12/9/55 *Payee Hugh M. Simmons

Per Hugh M. Simmons Title Owner

Hugh M. Simmons

*When a voucher is signed or receipted in the name of a company or corporation, the name of the person writing the company or corporate name, as well as the capacity in which he signs, must appear. For example: "John Doe Company, per John Smith, Secretary," or "Treasurer," as the case may be.

→ NOTE.—Title 18, U. S. Code (Crimes), section 1001, makes it a criminal offense to make a willfully false statement or representation to any department or agency of the United States as to any matter within its jurisdiction.

(Instructions on reverse)

Pursuant to authority vested in me, I certify that this account is correct and proper for payment in the amount of:

$1992.00

Signature _____
(Authorized Certifying Officer)

Date _____ Vou. No. SF-DMEA-22

(See other side)

(For Government use only)

CERTIFICATION BY GOVERNMENT REPRESENTATIVE:

I certify that to the best of my knowledge and belief the contractor submitting this voucher is operating a Defense Minerals Exploration Administration project under Contract No. Idm-E829 in accordance with the terms of the contract.

Signature Benjamin F. Sheehan John D. Marie Title Mining Engineer Date Dec. 12, 1955

APPROVAL BY DMEA EXECUTIVE OFFICER OR ALTERNATE:

Signature S. Ricker Title Executive Officer Date Dec. 12, 1955

MONTHLY REPORT OF OPERATOR

The Operator (Contractor) of an exploration project is required to make a monthly report to the Government through the Regional Executive Officer. This report consists of three parts as follows:

(a) *Form MF-104—Operator's Monthly Report and Voucher.*—This form details expenditures and constitutes a voucher for reimbursing the Operator for the Government's share of costs;

(b) *Form MF-104A—Operator's Unit Cost and Progress Report.*—This is a statistical report of expenditures which shows costs for the various types of operation; and

(c) *Narrative.*—A concise narrative description of progress made, results accomplished, and any unusual difficulties encountered must be furnished as an attachment to this Report and Voucher. Wherever possible, the narrative is to be illustrated with maps or sketches showing formations penetrated and location and assays of samples taken as well as advances in workings. In the case of diamond drilling or churn drilling, the location and inclination of holes is to be shown on a map; logs and assays also are to be submitted.

The Monthly Report of Operator should be prepared in an original and four copies all of which must be sent to the Executive Officer of the Region not later than the 15th of the month following.

Preparation of Form MF-104—Operator's Monthly Report and Voucher.—All the applicable spaces in Form MF-104 should be filled in by the Operator, and the Operator or his agent should sign the certification in the lower left corner of the form.

The items of costs are arranged in the order they appear in Article 6 (a) of Form MF-200 (Revised February 1952), however, this form is readily adaptable for use in reporting activities under other contract forms.

Under Item (1) delete words "Short Form" if the contract is a sub-contract under Form MF-200; and delete word "Independent" if the contract reported is on Form MF-200 (A). Also, report work paid for on a unit basis under contract Form MF-200 as though it were performed under an independent contract.

Under Item (2) include labor, supervision and technical services incurred for the exploratory operations. Do not include labor, supervision and technical services used for work performed under items (5) and (6).

Under Item (3) include the costs of material and supplies used in the project other than that used under items (5) and (6).

Under Item (4) appear the three types of operating equipment expenditures, that is, rental, purchase and depreciation. The expenditures made for renting equipment belonging to a third party will be reported under "Rental". The amount paid or duly obligated for payment for the purchase of equipment will be reported under "Purchase". The amount of expenditures due the Operator to reimburse him for depreciation of equipment owned will be reported under "Depreciation".

Item (5) comprises costs of labor, supervision, technical services, materials, etc., which are used in the initial rehabilitation and repair of existing buildings, installations, fixtures, and equipment. These costs, therefore, should not be reported under items (2) and (3).

Item (6) includes the labor, supervision, technical services, materials, etc., used in the installation or construction of new buildings, fixed improvements, etc., necessary for the project. These costs, therefore, should not be reported under items (2) and (3).

Item (7) covers miscellaneous types of expenditure such as payroll taxes, liability insurance, workmen's compensation insurance, repairs to equipment and sampling and analysis. Only that part of payroll taxes, liability insurance and workmen's compensation which are paid by the operator should be reported under item (7). The share paid by the employee as a payroll deduction is to be included under item (2) as labor costs.

Item (8) includes any unforeseen costs not included in the other seven categories.

The original of Form MF-104 when submitted for reimbursable expenses incurred under contract Form MF-200 must be supported by original documentation or by certified copies of purchase orders, payrolls or transcripts of payrolls, unless such documentation has been waived by the Regional Executive Officer. This certification may be stated thus, "Certified True Copy (or Transcript)", followed by appropriate signature. If the Executive Officer of the Region determines that a contract under Form MF-200 should have an "on-site" audit, that is, a Government auditor should make an audit of the Operator's books and records of account, the Operator need not support his monthly voucher with original or certified documents except in cases of equipment purchases whose individual costs exceed $50.00. In these cases the original or a certified copy of the purchase order or invoice should be attached to the Monthly Voucher. N. B.—Only the *original* of Form MF-104 is required to be documented. The four copies of Form MF-104 are not to be thus supported.

Form MF-104 submitted for reimbursement under fixed price contracts on Form MF-200 (A), however, are not required to be supported by documentation of any kind. The Operator will submit his claim under item (1) of Form MF-104 by deleting as stated above the word "Independent" and by showing the number of feet or other units immediately after the appropriate descriptive word, such as, drilling, bulldozing, crosscutting, drifting, etc., and giving the "Monthly Total" amount due. "Totals Previously Reported", and "Totals to Date" columns should also be filled in.

Form MF-104A
(April 1952)

Budget Bureau No. 42-R1151.2

UNITED STATES
DEPARTMENT OF THE INTERIOR

DEFENSE MINERALS EXPLORATION ADMINISTRATION

RECEIVED DEC 23 1955

OPERATOR'S UNIT COST AND PROGRESS REPORT

Month of Sept., Oct., November 19~~x~~55 Docket No. DMEA 3698 Contract No. Idm-E829

Operator's Name Hugh M. Simmons Minerals Mercury

Address 801 Alhambra Boulevard, Sacramento, Calif.

OPERATION	Unit	Costs This Month	Units This Month	Costs to Date	Units to Date	Unit Costs to Date	Authorized by Contract: Units	Authorized by Contract: Unit Costs
Stage II:								
Drifting & X-cutting	Ft.	2,460	82	2,460.00	82	30.00	440	30.00
Crosscutting								
Raising								
Shafts ~~xxx~~ Timbering	Ft.	196	28	196.00	28	7.00	300	7.00
Winze ~~xxxx~~ Sample Analysis	ea.	-	-	-	-	-	30	2.00
Drilling: Core								
Churn								
Stage I: Auger								
~~xxxxx~~ Stripping								
~~xxxxxx~~ Trenching Rehabilitation	Ft.	-	-	2,400.00	200	12.00	200	12.00
Test Pits ~~xxxxx~~ Sample Anlys.	ea.	-	-	-	-	-	20	2.00
Roads and Trails								
Total Distributed Costs		2,656.00	-	5,056.00				Total Costs Authorized by Contract
Operating Equipment Purchased					Stage I			2,440.00
Initial Rehabilitation and Repairs					Stage II			15,360.00
New Buildings, Improvements, etc.								
Total Costs		2,656.00		5,056.00				17,800.00

The undersigned company, and the official executing this certification on its behalf, hereby certify that the information contained in this report is correct and complete to the best of their knowledge and belief.

Date 12/9/55 Operator Hugh M. Simmons

Per Hugh M. Simmons Title Owner

Hugh M. Simmons

NOTE.—Title 18, U. S. Code (Crimes), section 1001, makes it a criminal offense to make a willfully false statement or representation to any department or agency of the United States as to any matter within its jurisdiction.

Remarks:

(Instructions on reverse)

(For Government use only)

INSTRUCTIONS

Preparation of Form MF-104A—Operator's Unit Cost and Progress Report.—Applicable places on Form 104A should be filled in by the Operator. The purpose of this form is twofold as follows: (1) to furnish the supervising engineers and other administrators with statistical information necessary to better determine the progress of the project; and (2) to furnish more permanent information on mining costs for future use. The more important phases of operation on which permanent information is desired have been outlined in the form. There are blank lines, however, for those unusual phases which may need to be reported for a particular project. It will be necessary for the Operator to distribute his costs among the applicable phases reported with the exception of three items the costs of which are not to be distributed by the Operator. These three items are: "Operating Equipment Purchased", "Initial Rehabilitation and Repairs", and "New Buildings, Improvements, etc." The reason for not distributing these items on a monthly basis is doubtless clear to the Operator, since such distribution might well overstate the cost for any one month or period short of the entire contract period.

Form MF-104A has been designed to tie in with Form MF-104 for both monthly and cumulative costs. The "Total Costs" on Form MF-104A for each month should equal the monthly "Total Costs" as reported on Form MF-104. This is also true of the "Total Costs To Date".

In preparing Form MF-104A, it will be necessary frequently to distribute certain costs over a number of items. For instance, supervisory and engineering costs may have to be distributed over several phases, such as, drifting, crosscutting, raising, etc., provided that these items were reported active for the month. Such distributions should be made on the basis of time spent on the various phases, on man days of labor charged to such phases, or on some other equitable basis. "Operating Equipment", "Initial Rehabilitation and Repairs", and "New Buildings Improvements, etc.", will be distributed to the several phases of the project by the Washington Office of DMEA at the close of the project if determined necessary. The last two columns headed "Authorized by Contract" will be filled in by the Operator if such information is found in the contract. This information is usually a part of Exhibit "A" of the contract. A space for remarks has been provided for the use of the Operator to call attention to any unusual circumstances causing excessive or disproportionate unit costs.

GPO 872894

Narrative Report

RECEIVED DEC 23 1955

Actual drifting operations on the lower adit level were begun October 1. Some delays were entailed in procuring and installation of mine plant operating equipment and recruiting sufficient labor.

Three precussion type long holes were drilled on the operator's account during the interim between completion of Stage I work and drifting work under Stage II. These holes were drilled northeastward from the lower adit level near the beginning of the drift to guide drifting and crosscutting work.

A progress map showing work to date will be prepared.

Contract work progress to date is as follows:

Stage I:	Rehabilitation	200 feet @ $12.00 a foot	$2,400.00
Stage II:	Drifting	82 feet @ $30.00 a foot	2,460.00
	Timbering	28 feet @ $ 7.00 a foot	196.00
		Totals to date	$5,056.00

Hugh M. Simmons

Hugh M. Simmons

Form MF-104 (Rev.)
(April 1952)

Budget Bureau No. 42-R1036.5

UNITED STATES
DEPARTMENT OF THE INTERIOR
DEFENSE MINERALS EXPLORATION ADMINISTRATION

ACCOUNTS SEP 7

OPERATOR'S MONTHLY REPORT AND VOUCHER

Month of July-August, 1955 Docket No. DMEA 3698 Contract No. Idm-E829

Operator's Name Hugh Michael Simmons Minerals Mercury

Address 801 Alhambra Blvd., Sacramento, Calif.

RECEIVED SEP 12 1955

Contract Amount, $ 17,800.00 Government Participation: 75 % Amount, $ 13,350.00

ITEMS OF COSTS	FOR OPERATOR'S USE			FOR GOVERNMENT USE ONLY		
	Monthly Total	Totals Previously Reported	Totals To Date	Approved Monthly Total	Approved Totals Previously Reported	Approved Totals To Date
(1) Independent Short Form Contracts:						
Drilling						
Bulldozing						
Crosscutting						
Drifting						
Rehabilitation	$2,400	None	$2,400.00			
(2) Labor and Supervision:						
Labor						
Supervision						
Technical Services						
(3) Operating Mat'ls. and Supplies:						
Timber						
Explosives						
Pipe						
Track						
(4) Operating Equipment:						
Rental						
Purchase						
Depreciation						
(5) Initial Rehabilitation and Repairs						
(6) New Bldgs., Improvements, etc.						
(7) Miscellaneous:						
Repairs to Equipment						
Sampling and Analysis	None	None	None			
Payroll Taxes						
Liability Insurance						
(8) Contingencies (specify):						
TOTALS	$2,400		$2,400.00			

I certify that the above bill is correct and just and that payment therefor has not been received.

Date 16 Aug. 55 *Payee Hugh M. Simmons, M.D.

Per _____ Title Owner

*When a voucher is signed or receipted in the name of a company or corporation, the name of the person writing the company or corporate name, as well as the capacity in which he signs, must appear. For example: "John Doe Company, per John Smith, Secretary," or "Treasurer," as the case may be.

NOTE.—Title 18, U. S. Code (Crimes), section 1001, makes it a criminal offense to make a willfully false statement or representation to any department or agency of the United States as to any matter within its jurisdiction.

(Instructions on reverse)

Pursuant to authority vested in me, I certify that this account is correct and proper for payment in the amount of:

$1800.00

Signature _____
(Authorized Certifying Officer)

Date SEP 8 1955 Vou. No. SF-DMEA-9

(See other side)

(For Government use only)

CERTIFICATION BY GOVERNMENT REPRESENTATIVE:

I certify that to the best of my knowledge and belief the contractor submitting this voucher is operating a Defense Minerals Exploration Administration project under Contract No. Idm-E829 in accordance with the terms of the contract.

Signature John D. Warne Title Mining Engineer Date 9/2/55

John D. Warne

APPROVAL BY DMEA EXECUTIVE OFFICER OR ALTERNATE: Executive Officer DMEA Field Team

Signature S. Ricker Title Region II Date 9/2/55

S. Ricker

MONTHLY REPORT OF OPERATOR

The Operator (Contractor) of an exploration project is required to make a monthly report to the Government through the Regional Executive Officer. This report consists of three parts as follows:

(a) *Form MF-104—Operator's Monthly Report and Voucher.*—This form details expenditures and constitutes a voucher for reimbursing the Operator for the Government's share of costs;

(b) *Form MF-104A—Operator's Unit Cost and Progress Report.*—This is a statistical report of expenditures which shows costs for the various types of operation; and

(c) *Narrative.*—A concise narrative description of progress made, results accomplished, and any unusual difficulties encountered must be furnished as an attachment to this Report and Voucher. Wherever possible, the narrative is to be illustrated with maps or sketches showing formations penetrated and location and assays of samples taken as well as advances in workings. In the case of diamond drilling or churn drilling, the location and inclination of holes is to be shown on a map; logs and assays also are to be submitted.

The Monthly Report of Operator should be prepared in an original and four copies all of which must be sent to the Executive Officer of the Region not later than the 15th of the month following.

Preparation of Form MF-104—Operator's Monthly Report and Voucher.—All the applicable spaces in Form MF-104 should be filled in by the Operator, and the Operator or his agent should sign the certification in the lower left corner of the form.

The items of costs are arranged in the order they appear in Article 6 (a) of Form MF-200 (Revised February 1952), however, this form is readily adaptable for use in reporting activities under other contract forms.

Under Item (1) delete words "Short Form" if the contract is a sub-contract under Form MF-200; and delete word "Independent" if the contract reported is on Form MF-200 (A). Also, report work paid for on a unit basis under contract Form MF-200 as though it were performed under an independent contract.

Under Item (2) include labor, supervision and technical services incurred for the exploratory operations. Do not include labor, supervision and technical services used for work performed under items (5) and (6).

Under Item (3) include the costs of material and supplies used in the project other than that used under items (5) and (6).

Under Item (4) appear the three types of operating equipment expenditures, that is, rental, purchase and depreciation. The expenditures made for renting equipment belonging to a third party will be reported under "Rental". The amount paid or duly obligated for payment for the purchase of equipment will be reported under "Purchase". The amount of expenditures due the Operator to reimburse him for depreciation of equipment owned will be reported under "Depreciation".

Item (5) comprises costs of labor, supervision, technical services, materials, etc., which are used in the initial rehabilitation and repair of existing buildings, installations, fixtures, and equipment. These costs, therefore, should not be reported under items (2) and (3).

Item (6) includes the labor, supervision, technical services, materials, etc., used in the installation or construction of new buildings, fixed improvements, etc., necessary for the project. These costs, therefore, should not be reported under items (2) and (3).

Item (7) covers miscellaneous types of expenditure such as payroll taxes, liability insurance, workmen's compensation insurance, repairs to equipment and sampling and analysis. Only that part of payroll taxes, liability insurance and workmen's compensation which are paid by the operator should be reported under item (7). The share paid by the employee as a payroll deduction is to be included under item (2) as labor costs.

Item (8) includes any unforeseen costs not included in the other seven categories.

The original of Form MF-104 when submitted for reimbursable expenses incurred under contract Form MF-200 must be supported by original documentation or by certified copies of purchase orders, payrolls or transcripts of payrolls, unless such documentation has been waived by the Regional Executive Officer. This certification may be stated thus, "Certified True Copy (or Transcript)", followed by appropriate signature. If the Executive Officer of the Region determines that a contract under Form MF-200 should have an "on-site" audit, that is, a Government auditor should make an audit of the Operator's books and records of account, the Operator need not support his monthly voucher with original or certified documents except in cases of equipment purchases whose individual costs exceed $50.00. In these cases the original or a certified copy of the purchase order or invoice should be attached to the Monthly Voucher. N. B.—Only the *original* of Form MF-104 is required to be documented. The four copies of Form MF-104 are not to be thus supported.

Form MF-104 submitted for reimbursement under fixed price contracts on Form MF-200 (A), however, are not required to be supported by documentation of any kind. The Operator will submit his claim under item (1) of Form MF-104 by deleting as stated above the word "Independent" and by showing the number of feet or other units immediately after the appropriate descriptive word, such as, drilling, bulldozing, crosscutting, drifting, etc., and giving the "Monthly Total" amount due. "Totals Previously Reported", and "Totals to Date" columns should also be filled in.

Form MF-104A
(April 1962)

Budget Bureau No. 42-R1151.2

UNITED STATES
DEPARTMENT OF THE INTERIOR

ACCOUNTS SEP 7 1955

DEFENSE MINERALS EXPLORATION ADMINISTRATION

RECEIVED SEP 12 1955

OPERATOR'S UNIT COST AND PROGRESS REPORT

Month of July-August 1955 Docket No. DMEA 3698 Contract No. Idm-E829

Operator's Name Hugh M. Simmons Minerals Mercury

Address 801 Alhambra Blvd., Sacramento, Calif.

OPERATION	Unit	Costs This Month	Units This Month	Costs to Date	Units to Date	Unit Costs to Date	Authorized by Contract: Units	Authorized by Contract: Unit Costs
STAGE II: Drifting and crosscut	Ft.	-	-	-	-	-	440	$30.00
~~Crosscutting~~ Timbering	Ft.	-	-	-	-	-	300	$ 7.00
Raising								
Shafts								
~~Winze~~ STAGE I Rehabilitation	Ft.	2,400	200	$2,400.00	200	12.00	200	$12.00
Drilling: Core								
Churn								
Auger								
Stripping								
~~Assaying~~ Sample Anal.	Ea.	-	-	-	-	-	20	$ 2.00
Test Pits								
Roads and Trails								
Total Distributed Costs								Total Costs Authorized by Contract
Operating Equipment Purchased								
Initial Rehabilitation and Repairs								
New Buildings, Improvements, etc.								
Total Costs		$2,400		$2,400.00				$17,800.00

The undersigned company, and the official executing this certification on its behalf, hereby certify that the information contained in this report is correct and complete to the best of their knowledge and belief.

Date 16 Aug. 55 Operator Hugh M. Simmons

Hugh M. Simmons, M.D.

Per _____ Title Owner

Remarks: Work under Stage I completed - no sample analysis charged.

NOTE.—Title 18, U. S. Code (Crimes), section 1001, makes it a criminal offense to make a willfully false statement or representation to any department or agency of the United States as to any matter within its jurisdiction.

(Instructions on reverse)

(For Government use only)

John D Warne

INSTRUCTIONS

Preparation of Form MF-104A—Operator's Unit Cost and Progress Report.—Applicable places on Form 104A should be filled in by the Operator. The purpose of this form is twofold as follows: (1) to furnish the supervising engineers and other administrators with statistical information necessary to better determine the progress of the project; and (2) to furnish more permanent information on mining costs for future use. The more important phases of operation on which permanent information is desired have been outlined in the form. There are blank lines, however, for those unusual phases which may need to be reported for a particular project. It will be necessary for the Operator to distribute his costs among the applicable phases reported with the exception of three items the costs of which are not to be distributed by the Operator. These three items are: "Operating Equipment Purchased", "Initial Rehabilitation and Repairs", and "New Buildings, Improvements, etc." The reason for not distributing these items on a monthly basis is doubtless clear to the Operator, since such distribution might well overstate the cost for any one month or period short of the entire contract period.

Form MF-104A has been designed to tie in with Form MF-104 for both monthly and cumulative costs. The "Total Costs" on Form MF-104A for each month should equal the monthly "Total Costs" as reported on Form MF-104. This is also true of the "Total Costs To Date".

In preparing Form MF-104A, it will be necessary frequently to distribute certain costs over a number of items. For instance, supervisory and engineering costs may have to be distributed over several phases, such as, drifting, crosscutting, raising, etc., provided that these items were reported active for the month. Such distributions should be made on the basis of time spent on the various phases, on man days of labor charged to such phases, or on some other equitable basis. "Operating Equipment", "Initial Rehabilitation and Repairs", and "New Buildings Improvements, etc.", will be distributed to the several phases of the project by the Washington Office of DMEA at the close of the project if determined necessary. The last two columns headed "Authorized by Contract" will be filled in by the Operator if such information is found in the contract. This information is usually a part of Exhibit "A" of the contract. A space for remarks has been provided for the use of the Operator to call attention to any unusual circumstances causing excessive or disproportionate unit costs.

GPO 872894

HUGH M. SIMMONS, M. D.
UROLOGY
801 ALHAMBRA BOULEVARD
SACRAMENTO 16, CALIFORNIA
TELEPHONE HILLCREST 5-8803

29 August 1955

RECEIVED
SEP 12 1955

Re: Docket No. DMEA-3698
Granada Quicksilver Mine
Napa County, California

S. Hicker
Executive Officer DMEA Field Team, Region 11
1605 Evens Ave.
Reno, Nevada

Dear Sir:

This is to inform you that I have now completed Stage I consisting of the rehabilitation of two hundred (200) feet of tunnel at the upper workings as agreed upon by contract with the DMEA.

This work has been performed in a good mining manner and has revealed the following information. Some high grade ore was removed from the muck pile while cleaning out the station as shown by map. The roof of the station shows many areas where colors of cinnabar stand out in the Franciscan sand stone. About ten feet in from the start of the north tunnel there is a vein of ore that shows a very promising show of cinnabar. There is a streak of black alta that is high grade, (138 lbs. per ton), along with a wider streak of low grade ore that pans well.

It is my opinion and the opinion of others that this may be the key to the ore body in this mountain, and we have every reason to believe that previous maps showing an ore shoot, 16ft X 60 Ft , will be found at the lower level, depth not as yet determined.

Sincerely

Hugh M. Simmons, M. D.

400

APR 26 1957

Mr. Hugh M. Simmons
801 Alhambra Boulevard
Sacramento, California

Re: Docket No. DMEA 3696 - Mercury
Granada Mine
Napa County, California
Contract No. Ida-329

Dear Mr. Simmons:

This is with reference to the subject exploration contract between you and the Government.

It is not our intention to issue a certification of discovery or development which would create a lien against the subject property. We are, therefore, closing our books with respect to this project. Your attention is called, however, to the provisions of the contract which require the operator to keep and preserve certain records for the period indicated.

We regret that the exploration work performed did not result in a discovery or development. Your participation in the exploration program, however, is sincerely appreciated.

Sincerely yours,

H. G. Mittendorf

Administrator

TL:Chapman:fcc
11/12/56
cc to: Docket
Code 400
Code 800
Admr. Read. File
FT. REG. II
Messrs. J. W. Bunningham, BEM
T. H. Killegaard, USGS

GOVERNMENT COPY

RECEIVED
AUG 15 1956

AMENDMENT NO. 1
TO
EXPLORATION PROJECT CONTRACT IDM-E824
DATED JUNE 28, 1955
DOCKET NO. DMEA-3698
BETWEEN
THE UNITED STATES OF AMERICA
AND
HUGH M. SIMMONS

It is agreed this 7th day of August, 1956 that the contract be amended as follows:

The completion date for work under the contract shall be extended from April 1, 1956 to May 30, 1956.

This amendment shall not be construed to increase the estimated total cost of the project, the aggregate amount which the Government may be required to contribute, nor the fixed unit cost of any item or work.

Executed in sextuplicate the day and year first above written.

THE UNITED STATES OF AMERICA

By _____
S. Ricker
Executive Officer
DMEA Field Team, Region II

HUGH M. SIMMONS

_____
Hugh M. Simmons

RECEIVED
AUG 15 1956

AMENDMENT NO. 1

Docket No. DMEA-3698 Mineral Mercury

Exploration Project Contract Idm-E829

Date of Contract June 28, 1955

Date of Amendment August 7, 1956

Operator Hugh M. Simmons

JUSTIFICATION

Project was delayed owing to cessation of work during the winter months on account of the inaccessibility of the property.

S. Ricker, Executive Officer
DMEA Field Team, Region III

Code 800

23 JUL 1956

Mr. Spangler Ricker, Executive Officer
DMEA Field Team, Region II
1605 Evans Avenue
Reno, Nevada

Re: Docket No. DMEA-3698, Mercury
Hugh M. Simmons
Granada Mine
Napa County, California
Contract No. Idm-E629

Dear Mr. Ricker:

Reference is made to your letter of April 23, 1956, in which you advised Mr. Simmons that the Government would not be justified in participating in more than 270 feet of drifting under Stage II of the contract.

Your letter of September 6, 1955, advised Mr. Simmons that the work permitted under Stage II of the contract would be limited to 220 feet of drifting and/or crosscutting.

To date we have received Forms MF-104 and MF-104A through February 1956, which showed 172 feet of drifting and 58 feet of timbering. No further forms or reports from the operator have been received in this office.

The interim report of March 19, 1956, by J. D. Warne, Bureau of Mines, advises that 210 feet of drifting had been carried out as of March 17, the date of inspection, and states that drifting should be carried on for an additional 20 feet. Apparently the operator was advised orally of this, as we do not have any copy of a letter to the operator.

The contract expired on April 1, 1956.

The interim report of April 12, 1956, by Donald B. Tatlock, Geological Survey, advises that 245 feet of drifting on Stage II had been completed as of April 4, the date of inspection.

The interim report of April 18, 1956, by D. B. Tatlock and E. H. Bailey, Geological Survey, advises that 247 feet of work had been completed as of April 12, the date of inspection. No work has been received in this office as to how and when the operator was advised that he could carry work beyond the 220-foot point. It was recommended that the operator be allowed to continue for another 31 feet.

As the contract expired on April 1, 1956, any work after this date would require an amendment. It is within your authority to write an amendment extending the time for completion of the contract.

Sincerely yours,

George C. Seifridge

Chairman, Operating Committee

APPROVED:

P. F. Yopes

Member, Bureau of Mines

Thor H. Kiilsgaard

Member, Geological Survey

cc: Docket
Code 400
Code 800
Oper. Comm.
Adm. Read. File
Thor Kiilsgaard, USGS
J. W. Pennington, USBM
FT, Reg. 2

TLChapman/ls
7/20/56

UNITED STATES
DEPARTMENT OF THE INTERIOR
DEFENSE MINERALS EXPLORATION ADMINISTRATION
WASHINGTON 25, D. C.

RECEIVED
SEP - 8 1955

1605 Evans Avenue
Reno, Nevada

September 6, 1955

Mr. Hugh M. Simmons
801 Alhambra Blvd.
Sacramento, California

Re: Docket No. DMEA-3698 - Uranium
Hugh M. Simmons
Granada Mine
Napa County, California
Contract No. Idm-E829

Dear Mr. Simmons:

You are hereby advised that you can proceed with Stage II of above referenced contract. Work permitted under Stage II consists of 220 feet of drifting and crosscutting as shown in red on attached plan. Any additional work under Stage II will depend on the results obtained from the 220 feet allowed.

Very truly yours,

S. Ricker
Executive Officer
DMEA Field Team, Region II

Attach.

SRicker:gh

cc: Finance Officer, Region II
Operating Committee, DMEA, Wash., D.C.
Geo. Mavor, Auditor, Region II
H. C. Miller, Region II
R. M. Smith, USGS
File

Contract No. Idm-E 829

Docket No. 369

DEPARTMENT OF THE INTERIOR

Terminated contract

DEFENSE MINERALS EXPLORATION ADMINISTRATION

TO: Chief, Finance Section, Budget and Finance Branch, Bureau of Mines

Please make the following entry on the records of the Defense Minerals Exploration Administration under the Strategic and Critical Minerals Exploration Program.

Date of Contract	Region	State	Commodity
June 28, 1955	II	California	Mercury

Name and Address of Operator: Hugh M. Simmons
801 Alhambra Boulevard
Sacramento, California

	Reserve	Obligation
Prior Amount	0	$13,350.00
Increase	0	0
Decrease	0	4,969.50
Revised Amount	0	$ 8,380.50

Remarks:

Allen S. Dakan, Chief
Operations Control and
Statistics Division
(Name)
(Title)

Date Delivered to Bureau of Mines, Washington 11/29/56

98963

Docket No. ~~DMEA - 3698~~

Commodity ~~Mercury~~

DEPARTMENT OF THE INTERIOR

DEFENSE MINERALS EXPLORATION ADMINISTRATION

STRATEGIC AND CRITICAL MINERALS EXPLORATION PROGRAM

TO: Chief, Finance Section, Budget and Finance Branch, Bureau of Mines

Please enter on the records of the Defense Minerals Exploration Administration under the Strategic and Critical Minerals Exploration Program, the following contract, or amendment to contract.

Contract No. Idm-E 829

Date of Contract ~~or Amendment~~ June 28, 1955

Name and Address of Operator:
Hugh M. Simmons
801 Alhambra Boulevard
Sacramento, California

Amount of Government participation $ 13,350.00

Percent of Government participation 75 %

Region: 11 State: California

(Name)
J. L. Chambers
Chief, Contract Administration and Audit Division

(Title)

Date Delivered to Bureau of Mines, Washington. 6/28/55

54458

Government's copy

RECEIVED

JUL 15 1955

MF-200A
(Revised June 1954)

Docket No. DMEA - 3698

Commodity Mercury

Contract No. Idm-E 829

UNITED STATES OF AMERICA
DEPARTMENT OF THE INTERIOR
DEFENSE MINERALS EXPLORATION ADMINISTRATION
EXPLORATION PROJECT CONTRACT[1]
(Short Form)

It is agreed this 28th day of June, 1955, between the United States of America, acting through the Department of the Interior, Defense Minerals Exploration Administration, hereinafter called the "Government," and [2] Hugh M. Simmons, whose mailing address is 801 Alhambra Boulevard, Sacramento, California, hereinafter called the "Operator," as follows:

ARTICLE 1. *This contract* is entered into under the authority of the Defense Production Act of 1950, as amended. It consists of this form (MF-200A), the attached Exhibit "A," Annex I, and 2 maps.

The Operator shall not transfer or assign this contract or any right thereunder without the written consent of the Government.

ARTICLE 2. *Operator's property rights.*—(a) The land which is the subject of this contract (hereinafter called "the land") is in the State of California, County of Napa, and is described in Annex I.[3]

(b) The Operator represents and undertakes that:

(1) The Operator is the [4] owner of [5] the entire interest in the land, in possession and entitled to possession for all of the purposes of this contract, under and by virtue of a [6] --, [7] recorded in Book --, page --, official records of said County; and

(2) The Operator's right, title, or interest (whether as owner, lessee, or otherwise) is subject only to the following claims, liens, or encumbrances: none

(c) The Subordination Agreement of the holder of any claim, lien, or encumbrance listed above, and (if the Operator does not hold the legal title) the Consent to Lien of any holder of the legal title of the land (lessor, seller, optionor, etc.), are attached, as follows:

[1] If sufficient space is not provided in any blank, use an extra sheet of paper and refer to it in the blank.
[2] Insert name, and if an organization, its nature (corporation and place of incorporation, partnership with names of partners, etc.).
[3] State on a separate sheet marked "Annex I" the legal description or enough to identify the property, particularly excluding any areas from which the production is not to be subject to the Government's percentage royalty.
[4] Insert "owner," "lessee," "contract purchaser," "locator," etc.
[5] Insert "the entire interest," "the mineral rights," "an undivided one-third," etc.
[6] Insert "deed," "lease," "contract," "location notice," "patent," etc.
[7] If not recorded, so indicate by inserting "un."

16—70618-3

(d) The Operator shall preserve and maintain his right, title, and interest in the land and his right to the possession thereof for the purposes of this contract, and shall devote the land and all existing improvements, facilities, buildings, installations, and appurtenances to the purposes of this contract. Until the lapse of the time within which the Government may make a certification of discovery or development without any such certification having been made, and after any such certification has been made, the Operator shall neither transfer, convey, nor surrender the land nor any right, title, or interest therein, nor permit nor suffer any claim, lien, or encumbrance thereon, without expressly referring to and providing in the instrument of conveyance, lien, or encumbrance for the preservation of the Government's right to a percentage royalty on production and lien for the payment thereof. If the Government makes no certification of discovery or development within the time limited in Article 7, it shall thereafter have no claim against the land or any production therefrom except for any production referred to in Article 7(b)(1).

ARTICLE 3. *The exploration project.*—The project is a search for indicated or undeveloped deposits of mercury. The work to be performed is described in Exhibit "A." The Operator on or before July 18-1955 shall commence the work, and on or before April 1, 1956 (unless the Operator's obligation to complete the work is terminated—see Article 8) shall complete the work.

ARTICLE 4. *Performance of the work.*—(a) *Operator's responsibility.*—The work shall be performed with reasonable diligence, efficiently, expertly, in a workmanlike manner, in accordance with good mining standards and State regulations for health and safety and for liability insurance covering employment; and with suitable and adequate equipment, facilities, materials, supplies, and labor, to bring it to completion within the time fixed.

(b) *Government may inspect.*—The Operator shall consult with and inform the Government on all phases of the work as it progresses. The Government may enter at all reasonable times to inspect the work under the contract, and also after a certification of discovery or development to inspect production operations and underground workings. The operator shall provide the Government with all reasonable means of access for such inspections.

ARTICLE 5. *Contribution by the Government.*—A fixed cost for each unit of work to be performed (per foot of drifting, per foot of drilling, per hour of operations, etc.) is hereby agreed upon, and is set forth in Exhibit "A" in connection with the estimated total cost of the project in the sum of $17,800.00 The Government will contribute 75 percent of the fixed unit costs as work is performed, in a total sum not in excess of $13,350.00: *Provided,* That until the Operator has rendered to the Government his final report, and any final auditing required by the Government has been made, and a final settlement of the contract has been made, the Government may withhold from the last voucher or vouchers such sums as it sees fit not in excess of 10 percent of the estimated total cost of the work. The Government will make its contribution on the basis of the monthly vouchers referred to in Article 6(b), but all payments by the Government are provisional only, subject to audit, until the account between the Operator and the Government is finally audited and settled. To the extent that excesses over fixed unit costs or any excess over the estimated total cost may be necessary for the performance of the work, the Operator shall incur and pay such excesses for his own account without contribution by the Government. The Government may make payments directly to independent contractors and suppliers for the account of the Operator rather than to the Operator.

ARTICLE 6. *Reports, accounts, audits.*—(a) *Operator's records.*—The Operator shall keep suitable records and accounts of the units of work performed and of any production in which the Government may have an interest; and shall preserve those with respect to work performed for at least three years after final payment by the Government, and those with respect to production for at least three years after any obligation to pay royalties to the Government has terminated. The Government may inspect and audit said records and accounts at any time, either by itself or by a certified public accountant. The Comptroller General of the United States or his representative, until the expiration of said three-year periods, shall have access to and the right to examine any pertinent books, documents, papers, and records of the Operator. All of the Operator's vouchers and records and accounts relating thereto and the Government's payments thereof remain subject to adjustment until final audit by the Government.

(b) *Progress reports and vouchers.*—The Operator shall provide the Government with five copies of monthly progress reports in three sections as follows: (1) Operator's Monthly Report and Voucher showing a detailed statement of units of work performed during the reporting period; (2) Operator's Unit Cost and Progress Report showing the various types of work performed during the reporting period and the fixed unit costs incurred for each type of work; and (3) a Narrative Report of the work

performed during the reporting period including adequate engineering-geological maps or sketches, drill hole logs and locations, and assay reports on samples taken concurrently with advance in mineralized ground. (Forms for reporting under (1) and (2) above will be provided by the Government.)

(c) *Final report.*—Upon completion of the work or termination of the Government's obligation to contribute to costs, the Operator shall furnish the Government with five copies of a final report (in addition to the final progress report and voucher). This final report shall include a geological and engineering evaluation of the results of the work performed under the contract with an estimate of the ore reserves resulting from such work, complete assay data, adequate geological and engineering maps or sketches, and a summary of the work performed and the unit costs thereof.

(d) *Report of sales.*—The Operator shall provide the Government with suitable accounting and documentary evidence covering all production to which the Government's percentage royalty relates, such as copies of smelter or concentrator settlement sheets, and certified accounts of production and sale or other disposition of production.

(e) *Compliance with requirements.*—If in the opinion of the Government any of the Operator's reports, records, or accounts are insufficient or incomplete, or if the Operator fails to make them, the Government may procure the making or completion of such with suitable attachments as an expense of the work to which the Operator shall contribute. The Government may withhold approval and payment of any vouchers relating to insufficient or incomplete reports, records or accounts.

ARTICLE 7. *Repayment by Operator.*—(a) *Certification.*—If the Government considers that a discovery or development from which production may be made has resulted from the work, the Government, at any time not later than six months after a sufficient final report and final account (see Article 6) has been rendered, may so certify in writing to the Operator. Such certification shall describe broadly or indicate the nature of the discovery or development.

(b) *Royalty on production.*—The Operator, as principal if the Operator is the producer, or as surety if the Operator is not the producer, shall pay to the Government a royalty on all minerals mined or produced from the land, as follows: (1) regardless of any certification of discovery or development, from the date of the contract until the lapse of the time within which the Government may make such certification, or until the total net amount contributed by the Government without interest is fully repaid, whichever occurs first; or (2) if the Government makes a certification of discovery or development, within a period of ten years from the date of the contract, or until the total net amount contributed by the Government without interest is fully repaid, whichever occurs first.

(c) *Basis for computation.*—The Government's royalty shall be a percentage of the gross proceeds (including any bonuses, premiums, allowances, or other benefits) from the production sold, in the form sold (ore, concentrates, metal, or equivalent), at the point of delivery (the f. o. b. point); *except,* that charges of *the buyer* arising in the regular course of business, and shown as deductions on the buyer's settlement sheets, on account of the cost of treatment processes performed by *the buyer,* sampling and assaying to determine the value of the production sold, and freight paid by *the buyer* to a carrier (not the Operator), shall be allowed as deductions in arriving at the "gross proceeds" as that term is used herein. Any costs of treatment processes, sampling or assaying, or transportation, performed or paid by the Operator or by anyone other than the buyer, are not deductible in arriving at the "gross proceeds" as that term is here used. The term "treatment processes," as here used, means those processes (such as milling, concentrating, smelting, refining, or equivalent) applied to the crude ore or other production after it is extracted from the ground, to put it into a commercially marketable form; excluding fabricating or manufacturing.

(d) *Unsold production.*—If any production (ore, concentrates, metal, or equivalent), after the lapse of six months from the date the ore was extracted from the ground, remains neither sold nor used by the Operator in integrated manufacturing or fabricating operations (for instance, if it is stockpiled), the Government, at its option, as long as it so remains, may require the computation and payment of its royalty on the value of such production in the form (ore, concentrates, metal, or equivalent) it is in when the Government elects to require computation and payment. If any production is used by the Operator in integrated manufacturing or fabricating operations before the Government makes its election, the Government's royalty on such production shall be computed on the value thereof in the form in which and at the time when it is so used. "Value" as here used means what is or would be gross income from mining operations for percentage depletion purposes in Federal income tax determination, or the market value, whichever is greater.

(e) *Percentages of royalty.*—The percentages of the Government's royalty shall be as follows:

One and one-half (1½) percent of amounts ("gross proceeds" or "value") not in excess of eight dollars ($8.00) per ton of production in the form in which sold, held, or used, plus one-half (½) percent for each additional full fifty cents ($0.50) by which such amounts exceed eight dollars ($8.00) per ton, but not in excess of five (5) percent of such amounts.

(For instance: the royalty on an amount of five dollars ($5.00) per ton would be one and one-half (1½) percent; on an amount of ten dollars ($10.00) per ton, three and one-half (3½) percent.)

(f) *Time for computation and payment.*—The Government's royalty shall be computed and paid currently upon each lot sold, held, or used in integrated operations, as the case may be, as above provided in this article.

(g) *Lien for payment.*—To secure the payment of its percentage royalty, there is hereby granted to the Government a lien upon the land or the Operator's interest in the land and upon any production of minerals therefrom, until the royalty claim is extinguished by lapse of time or is fully paid.

(h) *Notice to purchasers.*—The Operator shall give notice of the Government's claim for royalty to any purchaser of the production, and shall authorize and direct such purchaser to pay the royalty directly to the Government and to furnish the Government with copies of the settlement sheets. If the records of any production and sales or other disposition of production, whether the production is by the Operator or by others, are not made available to the Government, the amount of the royalty may be estimated by the Administrator, Defense Minerals Exploration Administration, or his successor, and his estimate thereof shall be final and binding upon the Operator.

(i) *No obligation to produce.*—Nothing in this contract is to be construed as imposing any obligation on the Operator or the Operator's successor in interest to engage in any production operations.

(j) *Government not obligated to buy.*—Nothing in this contract shall be construed as imposing any obligation on the Government to purchase any minerals mined or produced from the land.

ARTICLE 8. *Termination of the Government's obligations.*—(a) If in the opinion of the Government operations at any time have failed to achieve anticipated results that indicate the probability of making a worthwhile discovery, and in the opinion of the Government further operations are not justified, the Government may give the Operator written notice thereof, and thereupon the Government shall be free of all obligation to pay on account of units of work not then performed, and the Operator shall be free of all further obligation to prosecute the work other than such as may be necessary and incidental to winding up, reporting, and accounting.

(b) If in the opinion of the Government the Operator is in any manner in default under the terms of the contract, the Government may give the Operator written notice of such default with a specification of reasonable time within which the default must be cured; and if the Operator fails to cure such default as required, thereupon the Government shall be relieved of all obligation to pay on account of units of work not performed when the notice was given, and the Operator shall be free of all obligation to prosecute the work other than such as may be necessary and incidental to winding up, reporting, and accounting. The remedy provided for the Government in this paragraph "(b)" is in addition to any other remedy provided in this contract, and in addition to any other remedy the law may provide for breach of contract.

(c) The giving of any notice by the Government under the provisions of this Article 8 shall not affect the Government's rights as provided for in the contract with respect to a percentage royalty, and such rights shall be fully preserved.

ARTICLE 9. *Notices to be given by the Government* may be delivered to the Operator, or may be sent by registered mail addressed to the Operator at his mailing address stated in this contract. If mailed, notices are deemed to have been delivered five days after the date of mailing.

ARTICLE 10. *Officials not to benefit.*—No member of or delegate to Congress or resident commissioner shall be admitted to any share or part of this contract or to any benefit that may arise therefrom; but this provision shall not be construed to extend to this contract if made with a corporation for its general benefit.

ARTICLE 11. *Changes and added provisions.*—

Executed in sextuplicate the day and year first above written.

HUGH M. SIMMONS
(Operator)

By Hugh M Simmons

THE UNITED STATES OF AMERICA

By O P Mittenthorp
Administrator, Defense Minerals
Exploration Administration

I, ..., certify that I am the ..... secretary of the corporation named as Operator herein; that ..... who signed this contract on behalf of the Operator, was then ..... of said corporation; that said contract was duly signed for and in behalf of said corporation by authority of its governing body, and is within the scope of its corporate powers.

.....

[CORPORATE SEAL]

U. S. GOVERNMENT PRINTING OFFICE 16—70618-1

EXPLORATION PROJECT CONTRACT
HUGH M. SIMMONS
DOCKET NO. DMEA-3698

RECEIVED
JUL 7

ANNEX I

The land referred to in Article 2 of the contract form is described as follows:

The Southeast quarter of the southeast quarter of section 27;

The northeast quarter of the northeast quarter of section 34;

The north half of northwest quarter, and the northwest quarter of northeast quarter, of section 35.

All the land lies in T. 10 N., R. 6 W., M.D.B.&M., and is in the Mayacmas Mining District.

RECEIVED
JUL 1 [illegible]

EXPLORATION PROJECT CONTRACT
HUGH M. SIMMONS
DOCKET NO. DMEA-3698

EXHIBIT "A"

Description of the Work

Figure 1 shows location of the property in Napa County, California.

Figure 2 shows mine workings and proposed rehabilitation and exploration work.

The work is divided into two stages. The Operator shall perform Stage I, and shall perform so much of the work set forth under Stage II as is approved in writing in advance by the Government.

Stage I

Rehabilitate 200 feet of the upper adit, as shown on Figure 2.

Any mineralized zones shall be sampled and assays made for mercury.

Stage II

Drift and crosscut 440 feet in the lower adit, as shown in Figure 2. The drift and crosscut shall have minimum dimensions of 4½ feet by 6½ feet in the clear of timber.

Any mineralized zones shall be sampled and assays made for mercury.

* * * * *

All work shall be timbered as necessary.

The location, direction, and extent of all work are subject to the approval of the Government.

Fixed Unit Costs

(The unit costs include all costs whatsoever necessary to complete the work.)

Stage I		
200 feet of rehabilitation @ $12.00/ft.	$ 2,400.00	
20 sample analyses @ $2.00/each sample	40.00	
Estimated Total Cost of Stage I		$ 2,440.00
Stage II		
440 feet of drifting and cross-cutting @ $30.00/ft.	13,200.00	
300 feet of timbering @ $7.00/ft.	2,100.00	
30 sample analyses @ $2.00/each sample	60.00	
Estimated Total Cost of Stage II		15,360.00
Estimated Total Cost of Project		$17,800.00
Government Participation @ 75%		$13,350.00

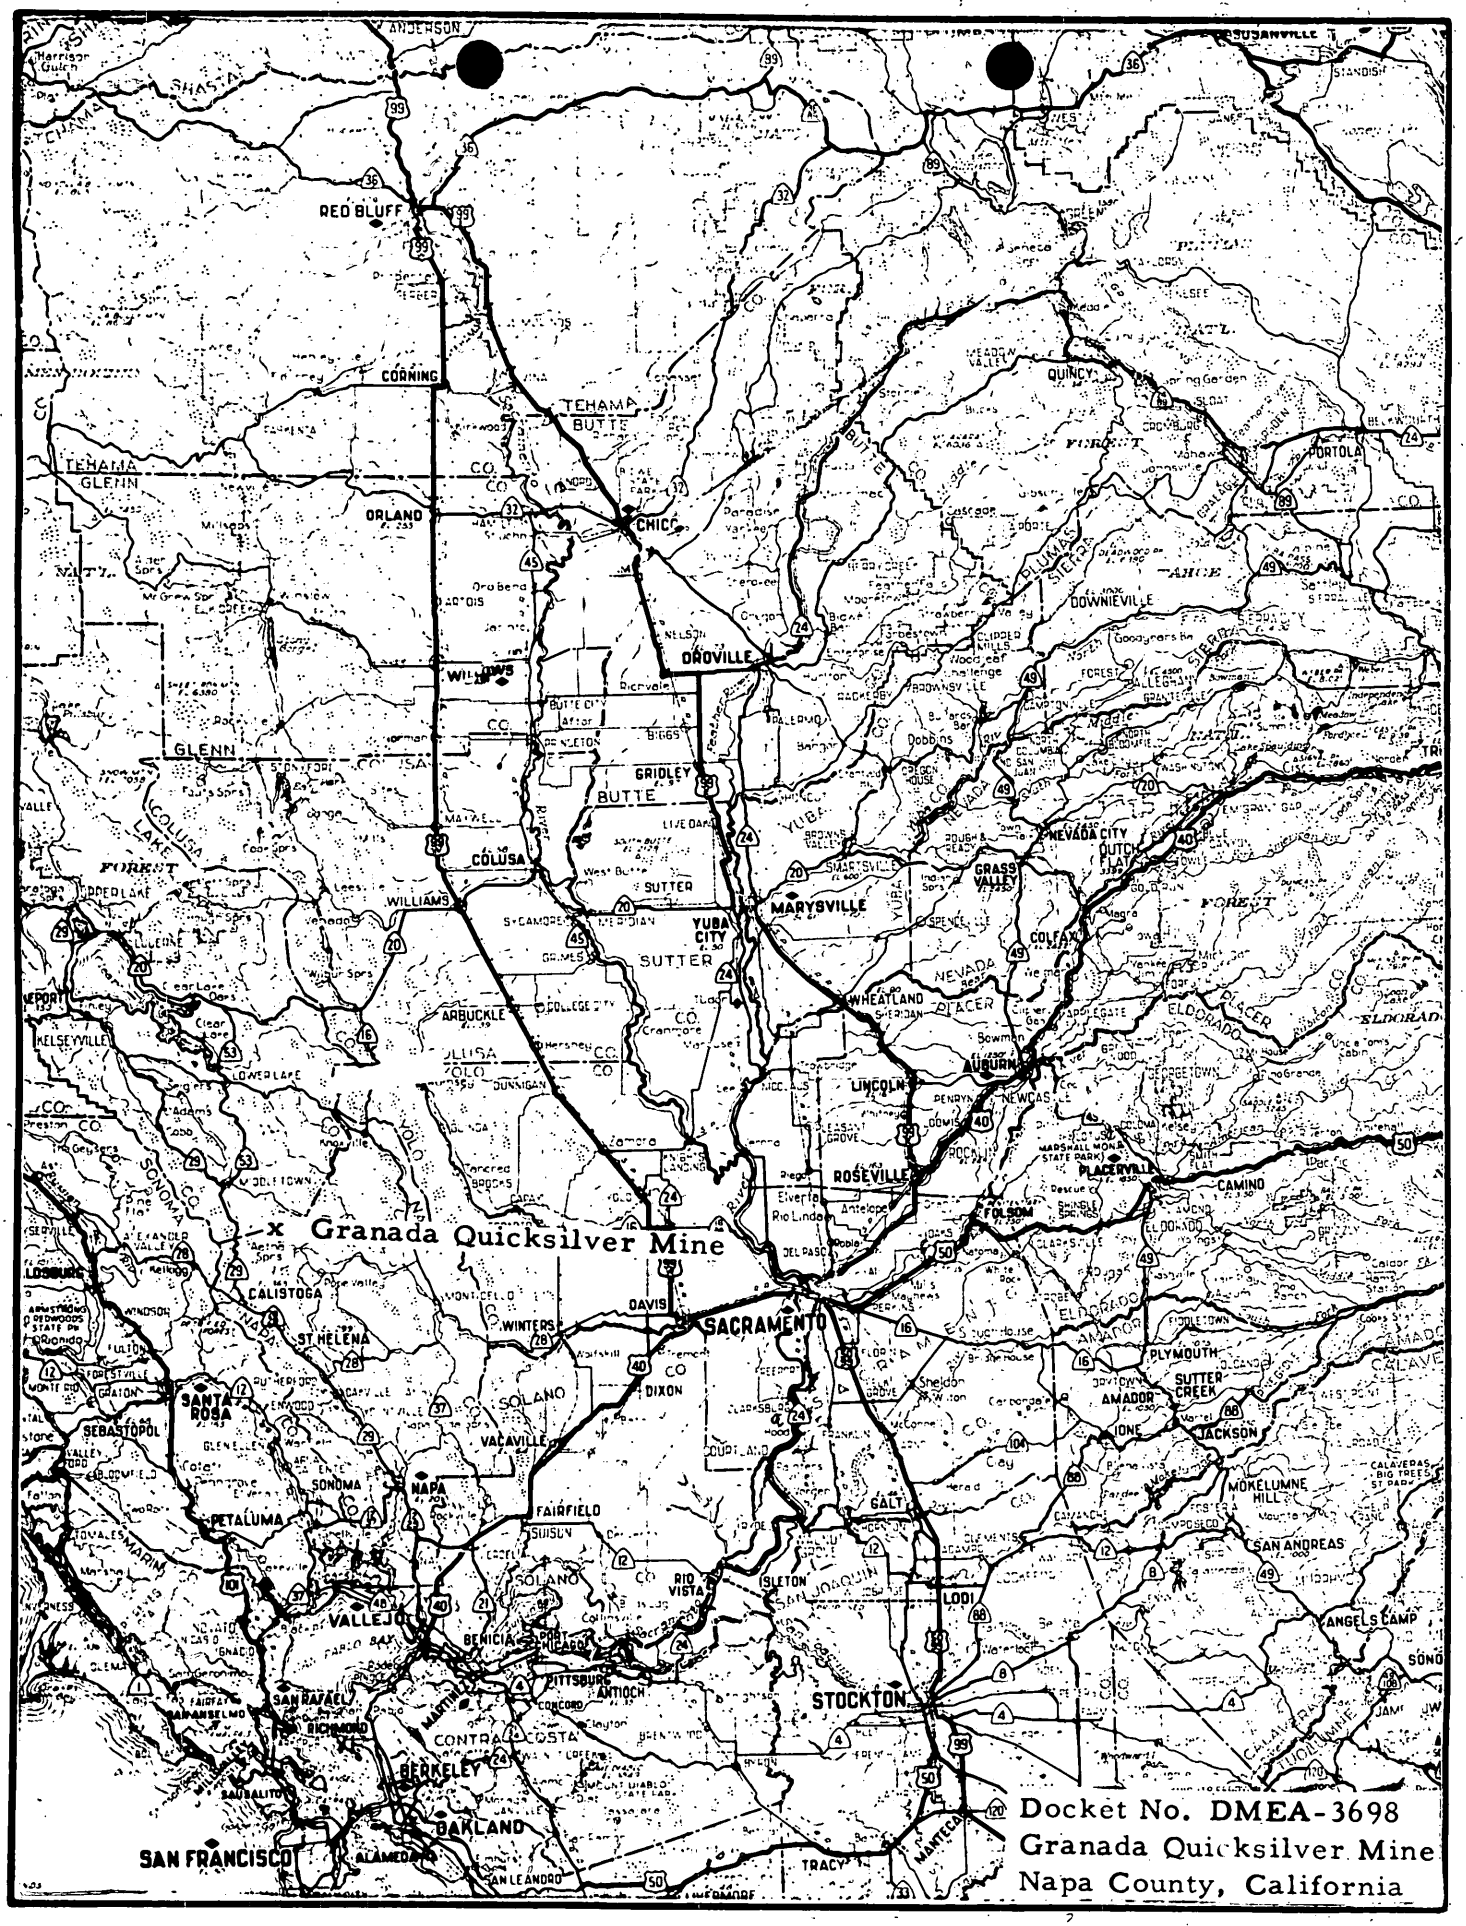

FIG. 1 LOCATION MAP

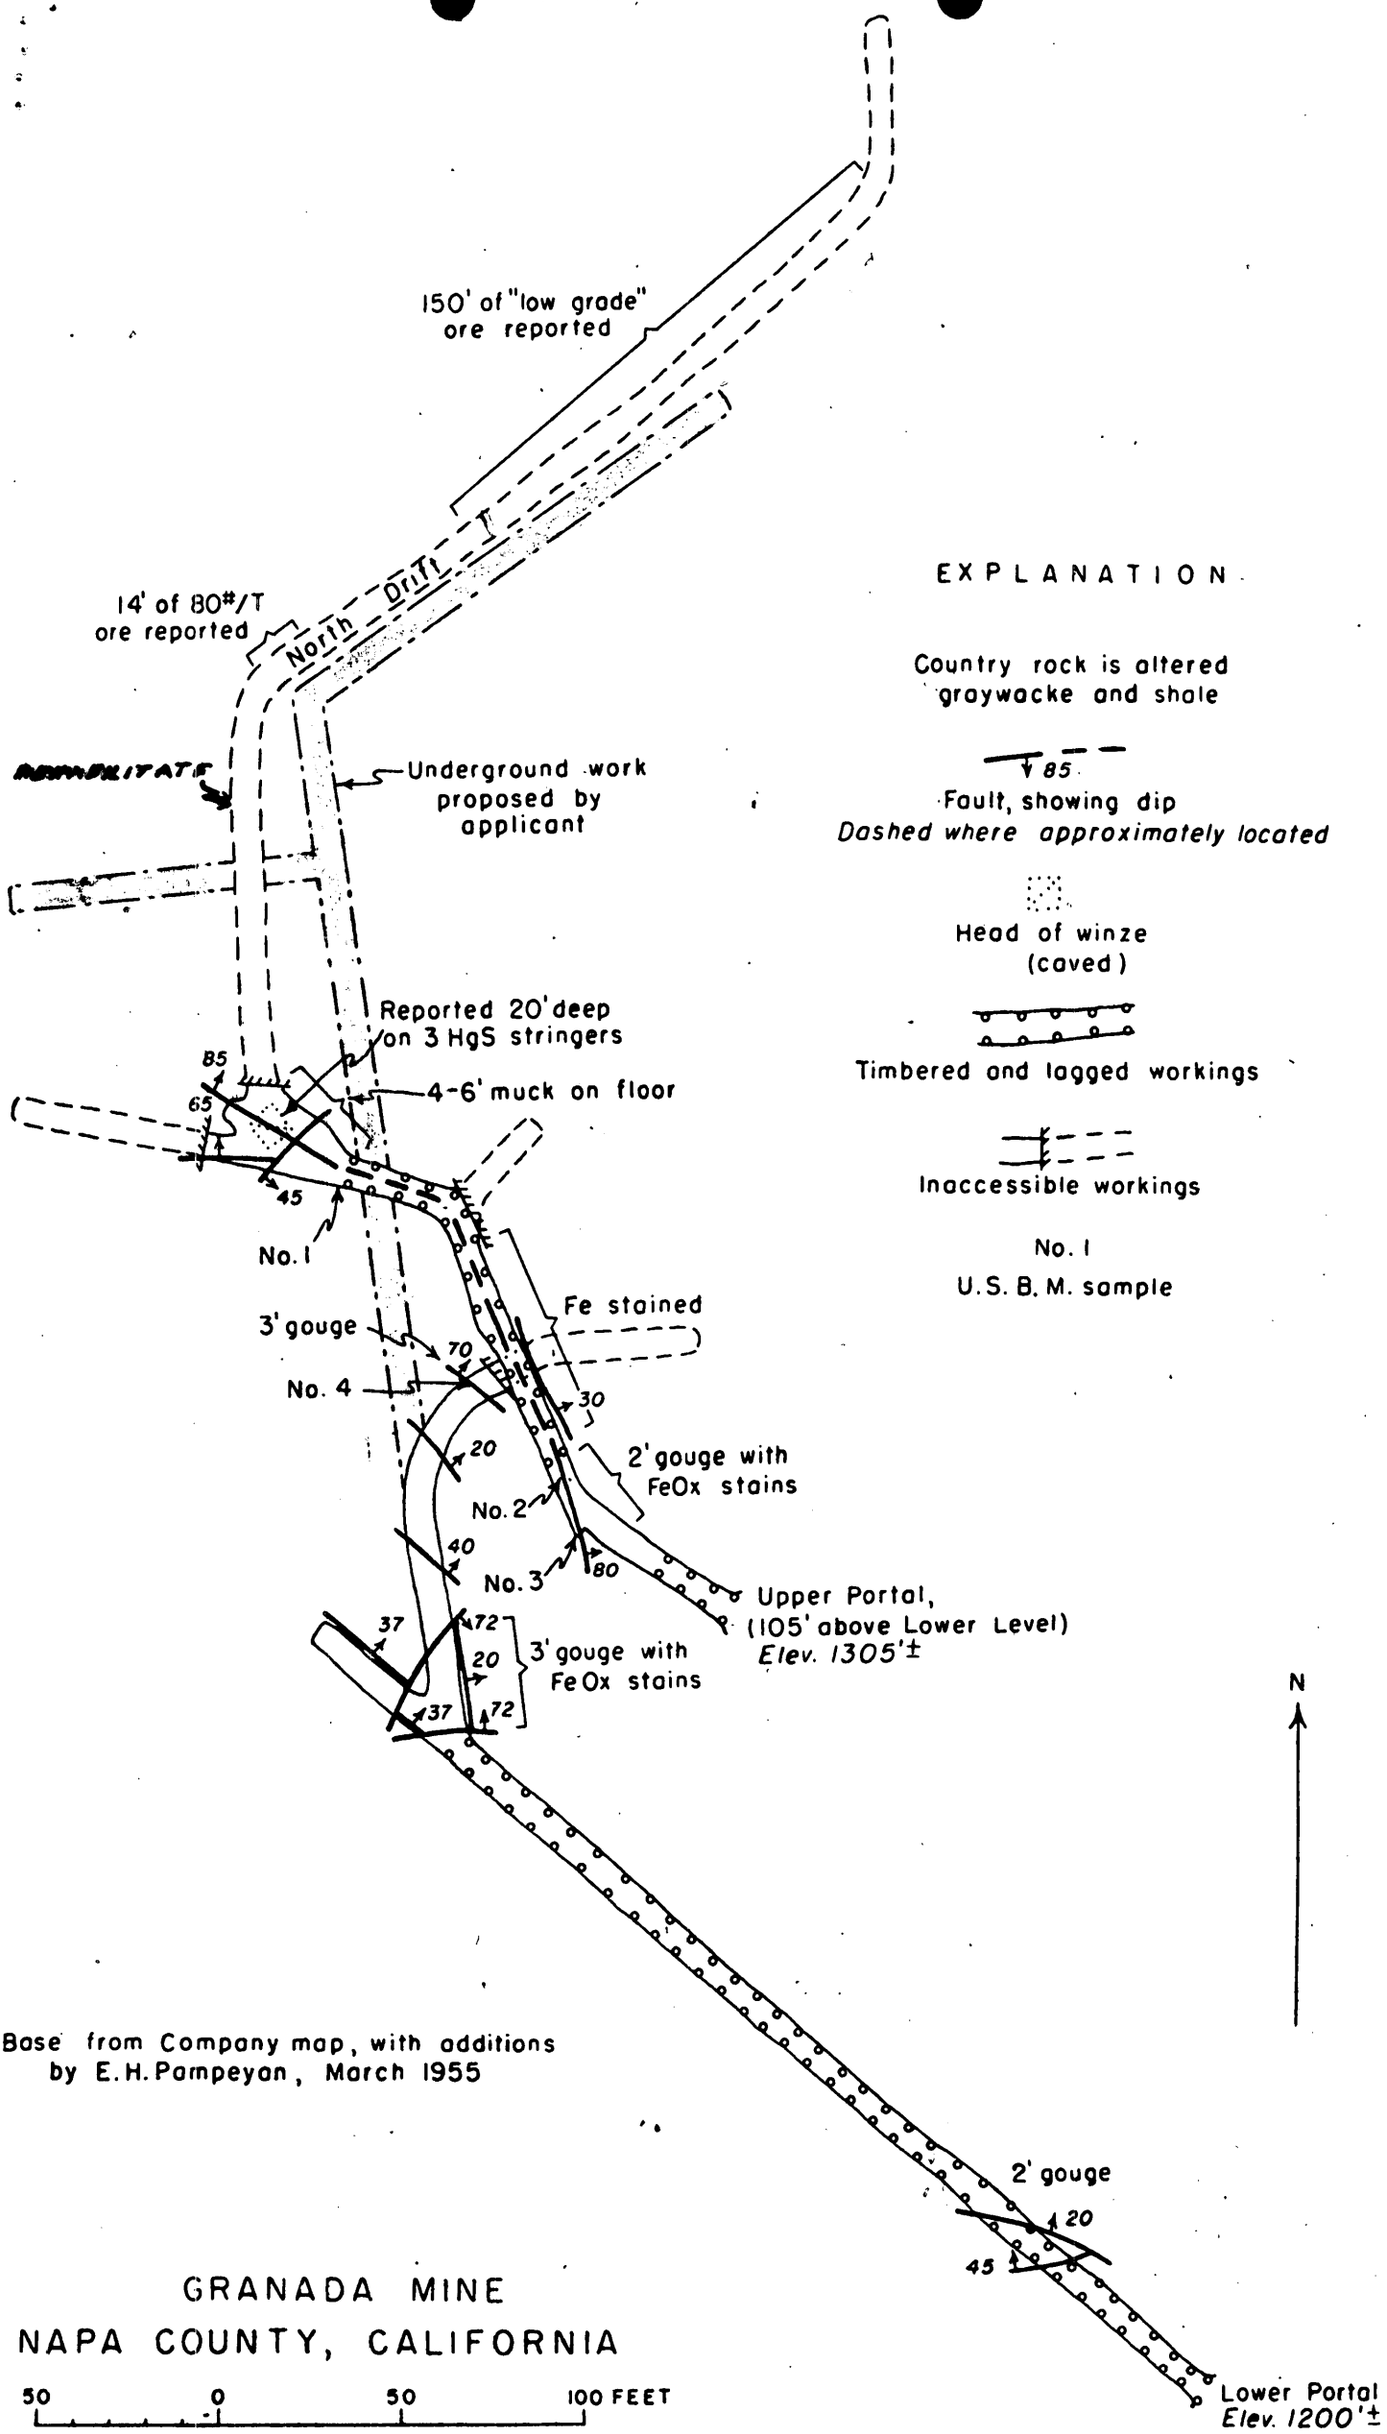

GRANADA MINE
NAPA COUNTY, CALIFORNIA

Figure 2
